



## **Lama Saleh – Work Samples**


### Building and Park Construction

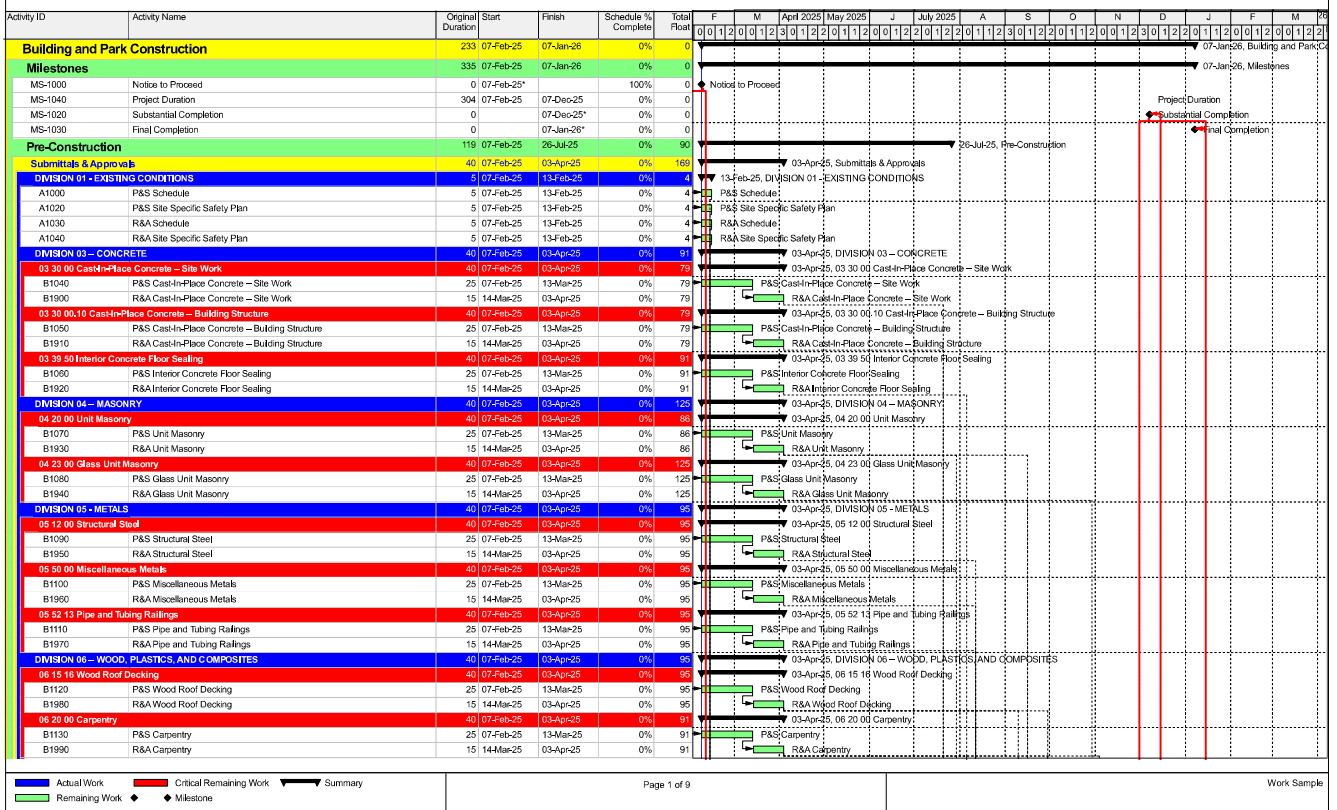

### Building and Park Construction

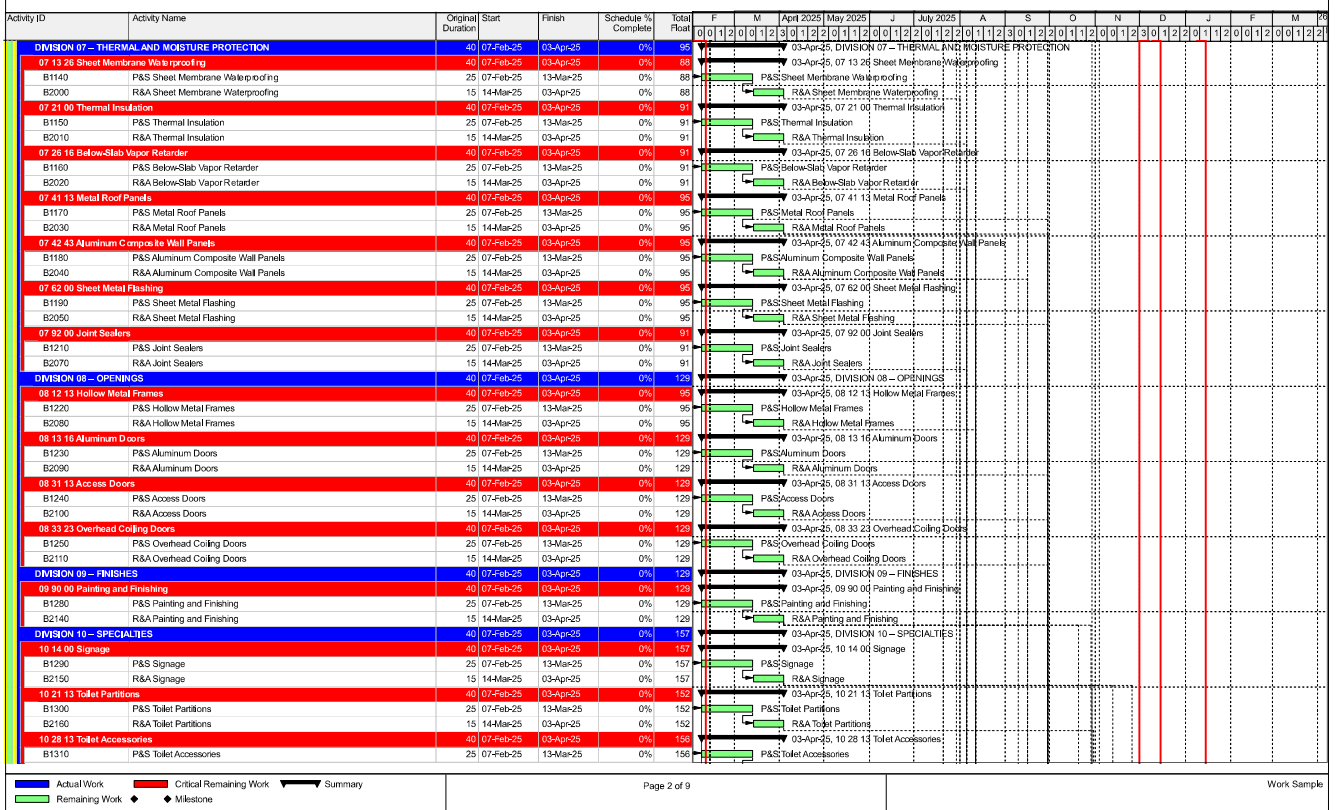


### Building and Park Construction

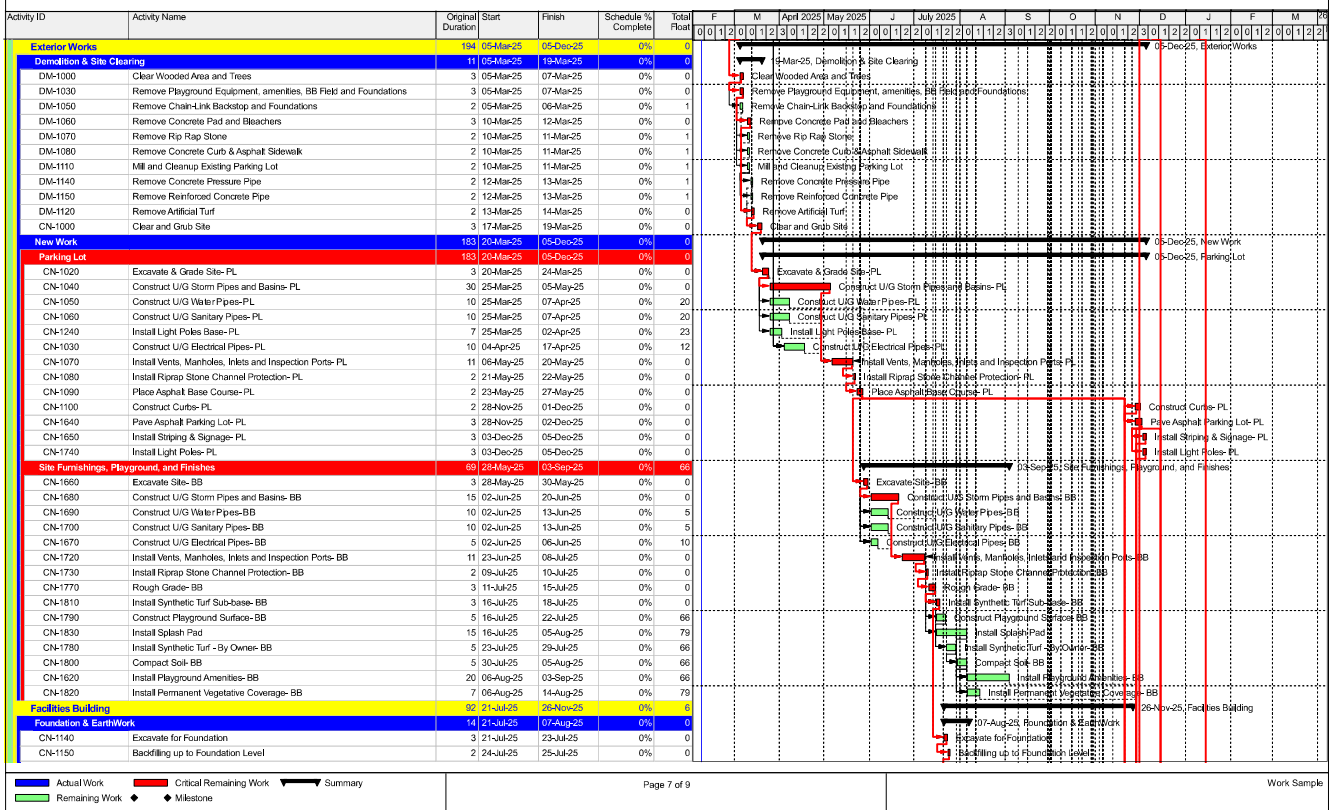

Page 7 of 9

Work Sample

### Building and Park Construction

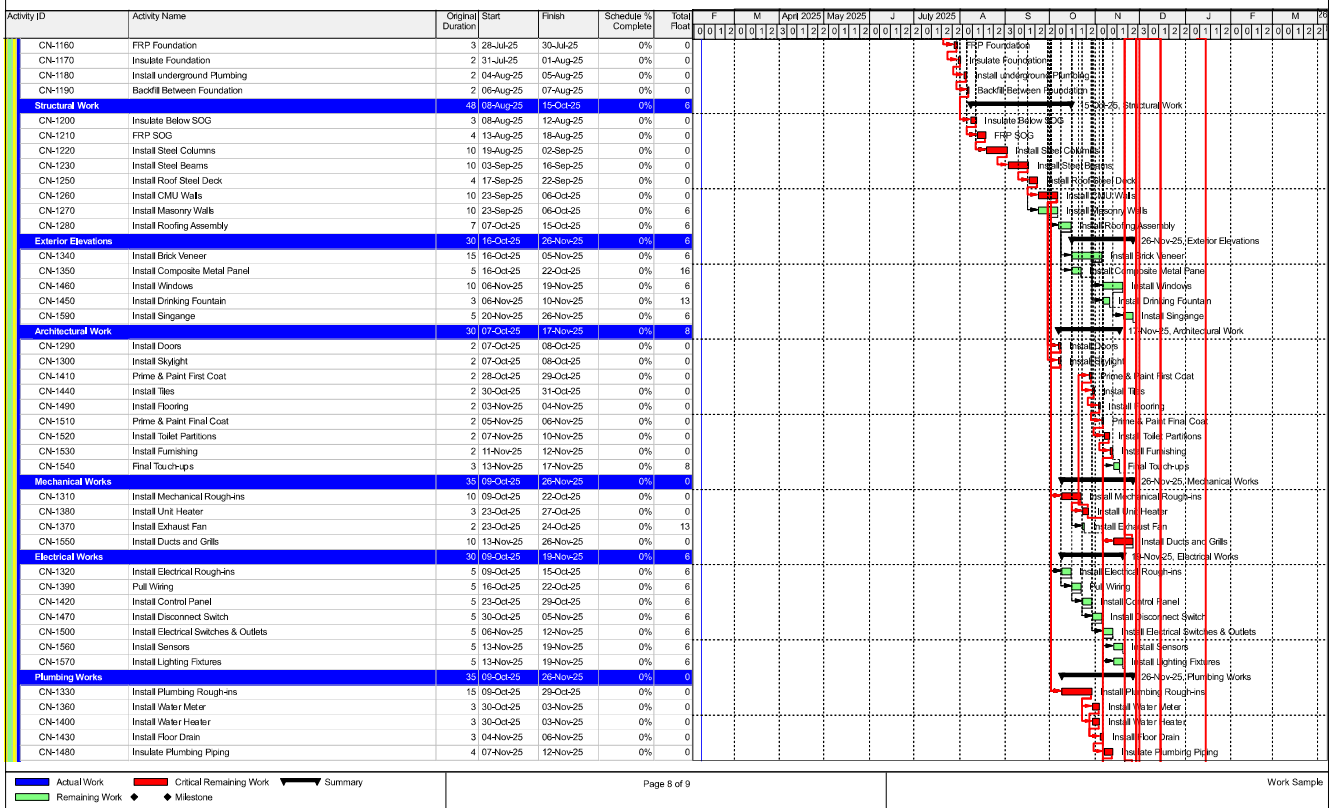

Page 8 of 9

Work Sample

Building and Park Construction

| Activity ID                        | Activity Name                             | Original Duration | Start     | Finish    | Schedule % Complete | Total Float | F | M | April 2025 | May 2025 | J | July 2025 | A | S | O | N | D | J | F | M | A |
|------------------------------------|-------------------------------------------|-------------------|-----------|-----------|---------------------|-------------|---|---|------------|----------|---|-----------|---|---|---|---|---|---|---|---|---|
| CN-1580                            | Install Plumbing Fixtures and Accessories | 10                | 13-Nov-25 | 26-Nov-25 | 0%                  | 0           | 0 | 1 | 2          | 0        | 0 | 1         | 2 | 3 | 0 | 1 | 2 | 3 | 0 | 1 | 2 |
| <b>Testing &amp; Commissioning</b> |                                           |                   |           |           |                     |             |   |   |            |          |   |           |   |   |   |   |   |   |   |   |   |
| TC-1000                            | Testing & Balancing                       | 2                 | 28-Nov-25 | 01-Dec-25 | 0%                  | 1           |   |   |            |          |   |           |   |   |   |   |   |   |   |   |   |
| TC-1020                            | Commissioning of System                   | 3                 | 02-Dec-25 | 04-Dec-25 | 0%                  | 1           |   |   |            |          |   |           |   |   |   |   |   |   |   |   |   |
| <b>Close-out</b>                   |                                           |                   |           |           |                     |             |   |   |            |          |   |           |   |   |   |   |   |   |   |   |   |
| CO-1040                            | Issue TCO                                 | 2                 | 06-Dec-25 | 07-Dec-25 | 0%                  | 0           |   |   |            |          |   |           |   |   |   |   |   |   |   |   |   |
| CO-1000                            | Punch-list                                | 5                 | 08-Dec-25 | 12-Dec-25 | 0%                  | 0           |   |   |            |          |   |           |   |   |   |   |   |   |   |   |   |
| CO-1010                            | Final Inspection                          | 5                 | 15-Dec-25 | 19-Dec-25 | 0%                  | 0           |   |   |            |          |   |           |   |   |   |   |   |   |   |   |   |
| CO-1020                            | Final Clean Up                            | 5                 | 22-Dec-25 | 29-Dec-25 | 0%                  | 0           |   |   |            |          |   |           |   |   |   |   |   |   |   |   |   |
| CO-1030                            | Demobilization                            | 6                 | 30-Dec-25 | 07-Jan-26 | 0%                  | 0           |   |   |            |          |   |           |   |   |   |   |   |   |   |   |   |

Actual Work Critical Remaining Work Summary  
Remaining Work Milestone

Page 9 of 9

Work Sample

Road Modifications

| Activity ID                | Activity Name                                      | Original Duration | Start      | Finish     | Schedule % Complete | Total Float | January 2025 | F | March 2025 | April 2025 | May 2025 | June 2025 | July 2025 | August 2025 | S | O | N | D |
|----------------------------|----------------------------------------------------|-------------------|------------|------------|---------------------|-------------|--------------|---|------------|------------|----------|-----------|-----------|-------------|---|---|---|---|
| <b>Road Modifications</b>  |                                                    |                   |            |            |                     |             |              |   |            |            |          |           |           |             |   |   |   |   |
| <b>Project Milestones</b>  |                                                    | 154               | 17-Jan-25  | 11-Sep-25  | 0%                  | 0           |              |   |            |            |          |           |           |             |   |   |   |   |
| ML-1010                    | NTP                                                | 0                 | 17-Jan-25* | 11-Sep-25* | 100%                | 0           |              |   |            |            |          |           |           |             |   |   |   |   |
| ML-1020                    | Substantial Completion                             | 0                 |            | 11-Sep-25* | 0%                  | 0           |              |   |            |            |          |           |           |             |   |   |   |   |
| ML-1030                    | Final Completion                                   | 0                 |            | 11-Sep-25* | 0%                  | 0           |              |   |            |            |          |           |           |             |   |   |   |   |
| <b>Permits</b>             |                                                    | 10                | 17-Jan-25  | 26-Jan-25  | 0%                  | 45          |              |   |            |            |          |           |           |             |   |   |   |   |
| PER-1000                   | NTA Highway Occupancy Permit                       | 10                | 17-Jan-25  | 26-Jan-25  | 0%                  | 45          |              |   |            |            |          |           |           |             |   |   |   |   |
| PER-1010                   | Soil Erosion and Sediment Control Certification    | 10                | 17-Jan-25  | 26-Jan-25  | 0%                  | 45          |              |   |            |            |          |           |           |             |   |   |   |   |
| <b>Pre-construction</b>    |                                                    | 80                | 17-Jan-25  | 06-Apr-25  | 0%                  | 115         |              |   |            |            |          |           |           |             |   |   |   |   |
| <b>Buyout</b>              |                                                    | 80                | 17-Jan-25  | 06-Apr-25  | 0%                  | 115         |              |   |            |            |          |           |           |             |   |   |   |   |
| <b>Milling/Asphalt</b>     |                                                    | 60                | 17-Jan-25  | 17-Mar-25  | 0%                  | 42          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1000                    | Buyout Milling/Asphalt - Subcontractor             | 30                | 17-Jan-25  | 15-Feb-25  | 0%                  | 42          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1100                    | Prepare & Submit Milling/Asphalt - Subcontractor   | 15                | 16-Feb-25  | 02-Mar-25  | 0%                  | 42          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1200                    | Review & Approve Milling/Asphalt - Subcontractor   | 15                | 03-Mar-25  | 17-Mar-25  | 0%                  | 42          |              |   |            |            |          |           |           |             |   |   |   |   |
| <b>Construction Sign</b>   |                                                    | 35                | 17-Jan-25  | 20-Feb-25  | 0%                  | 20          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1010                    | Buyout Construction Sign - Subcontractor           | 15                | 17-Jan-25  | 31-Jan-25  | 0%                  | 20          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1110                    | Prepare & Submit Construction Sign - Subcontractor | 10                | 01-Feb-25  | 10-Feb-25  | 0%                  | 20          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1210                    | Review & Approve Construction Sign - Subcontractor | 10                | 11-Feb-25  | 20-Feb-25  | 0%                  | 20          |              |   |            |            |          |           |           |             |   |   |   |   |
| <b>Fencing</b>             |                                                    | 80                | 17-Jan-25  | 06-Apr-25  | 0%                  | 115         |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1030                    | Buyout Fencing - Subcontractor                     | 50                | 17-Jan-25  | 07-Mar-25  | 0%                  | 115         |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1130                    | Prepare & Submit Fencing - Subcontractor           | 15                | 08-Mar-25  | 22-Mar-25  | 0%                  | 115         |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1230                    | Review & Approve Fencing - Subcontractor           | 15                | 23-Mar-25  | 06-Apr-25  | 0%                  | 115         |              |   |            |            |          |           |           |             |   |   |   |   |
| <b>Guide Rail</b>          |                                                    | 60                | 17-Jan-25  | 17-Mar-25  | 0%                  | 39          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1040                    | Buyout Guide Rail - Subcontractor                  | 30                | 17-Jan-25  | 15-Feb-25  | 0%                  | 39          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1140                    | Prepare & Submit Guide Rail - Subcontractor        | 15                | 16-Feb-25  | 02-Mar-25  | 0%                  | 39          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1240                    | Review & Approve Guide Rail - Subcontractor        | 15                | 03-Mar-25  | 17-Mar-25  | 0%                  | 39          |              |   |            |            |          |           |           |             |   |   |   |   |
| <b>Landscaping</b>         |                                                    | 60                | 17-Jan-25  | 17-Mar-25  | 0%                  | 46          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1050                    | Buyout Landscaping - Subcontractor                 | 30                | 17-Jan-25  | 15-Feb-25  | 0%                  | 46          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1150                    | Prepare & Submit Landscaping - Subcontractor       | 15                | 16-Feb-25  | 02-Mar-25  | 0%                  | 46          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1250                    | Review & Approve Landscaping - Subcontractor       | 15                | 03-Mar-25  | 17-Mar-25  | 0%                  | 46          |              |   |            |            |          |           |           |             |   |   |   |   |
| <b>Electrical</b>          |                                                    | 60                | 17-Jan-25  | 17-Mar-25  | 0%                  | 44          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1060                    | Buyout Electrical - Subcontractor                  | 30                | 17-Jan-25  | 15-Feb-25  | 0%                  | 44          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1160                    | Prepare & Submit Electrical - Subcontractor        | 15                | 16-Feb-25  | 02-Mar-25  | 0%                  | 44          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1260                    | Review & Approve Electrical - Subcontractor        | 15                | 03-Mar-25  | 17-Mar-25  | 0%                  | 44          |              |   |            |            |          |           |           |             |   |   |   |   |
| <b>Rumble Strip</b>        |                                                    | 60                | 17-Jan-25  | 17-Mar-25  | 0%                  | 50          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1070                    | Buyout Rumble Strip - Subcontractor                | 30                | 17-Jan-25  | 15-Feb-25  | 0%                  | 50          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1170                    | Prepare & Submit Rumble Strip - Subcontractor      | 15                | 16-Feb-25  | 02-Mar-25  | 0%                  | 50          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1270                    | Review & Approve Rumble Strip - Subcontractor      | 15                | 03-Mar-25  | 17-Mar-25  | 0%                  | 50          |              |   |            |            |          |           |           |             |   |   |   |   |
| <b>Permanent Sign</b>      |                                                    | 60                | 17-Jan-25  | 17-Mar-25  | 0%                  | 50          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1080                    | Buyout Permanent Sign - Subcontractor              | 30                | 17-Jan-25  | 15-Feb-25  | 0%                  | 50          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1180                    | Prepare & Submit Permanent Sign - Subcontractor    | 15                | 16-Feb-25  | 02-Mar-25  | 0%                  | 50          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1280                    | Review & Approve Permanent Sign - Subcontractor    | 15                | 03-Mar-25  | 17-Mar-25  | 0%                  | 50          |              |   |            |            |          |           |           |             |   |   |   |   |
| <b>Striping</b>            |                                                    | 60                | 17-Jan-25  | 17-Mar-25  | 0%                  | 50          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1090                    | Buyout Striping - Subcontractor                    | 30                | 17-Jan-25  | 15-Feb-25  | 0%                  | 50          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1190                    | Prepare & Submit Striping - Subcontractor          | 15                | 16-Feb-25  | 02-Mar-25  | 0%                  | 50          |              |   |            |            |          |           |           |             |   |   |   |   |
| PC-1290                    | Review & Approve Striping - Subcontractor          | 15                | 03-Mar-25  | 17-Mar-25  | 0%                  | 50          |              |   |            |            |          |           |           |             |   |   |   |   |
| <b>Material Submittals</b> |                                                    | 60                | 17-Jan-25  | 17-Mar-25  | 0%                  | 44          |              |   |            |            |          |           |           |             |   |   |   |   |

Actual Work Critical Remaining Work Summary  
Remaining Work Milestone

Page 1 of 5

Work Sample

### Road Modifications

| Activity ID                                     | Activity Name                                     | Original Duration | Start     | Finish    | Schedule % Complete | Total Float | January 2025 | February 2025 | March 2025 | April 2025 | May 2025 | June 2025 | July 2025 | August 2025 | S | O | N | D |
|-------------------------------------------------|---------------------------------------------------|-------------------|-----------|-----------|---------------------|-------------|--------------|---------------|------------|------------|----------|-----------|-----------|-------------|---|---|---|---|
| CON-2020                                        | Install Temporary Pavement Marking Tape           | 1                 | 13-May-25 | 14-May-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2080                                        | MII Existing Pavement                             | 1                 | 14-May-25 | 15-May-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2090                                        | Resurface Pavement                                | 1                 | 15-May-25 | 16-May-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2150                                        | Reconstruct Inlets                                | 1                 | 16-May-25 | 17-May-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2140                                        | Remove Soil Erosion and Sediment Control Devices  | 1                 | 16-May-25 | 17-May-25 | 0%                  | 12          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2130                                        | Remove Masking and Install New Pavement Markings  | 1                 | 18-May-25 | 20-May-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| STAGE 5B - NSO ROADWAY RESURFACING - Right Lane |                                                   |                   |           |           |                     |             |              |               |            |            |          |           |           |             |   |   |   |   |
| Pre-Stage 5B                                    |                                                   |                   |           |           |                     |             |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2170                                        | Install and Maintain MPT Devices                  | 9                 | 20-May-25 | 05-Jun-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2190                                        | Close Multi Right NSO & Right Half Ramp TSO       | 1                 | 20-May-25 | 21-May-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2180                                        | Install Soil Erosion and Sediment Control Devices | 2                 | 21-May-25 | 28-May-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2210                                        | Clear and Grub                                    | 1                 | 28-May-25 | 29-May-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| Stage 5B Construction                           |                                                   |                   |           |           |                     |             |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2200                                        | Removing and Masking Existing Pavement Markings   | 1                 | 29-May-25 | 30-May-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2220                                        | Install Temporary Pavement Marking Tape           | 1                 | 29-May-25 | 30-May-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2230                                        | MII Existing Pavement                             | 1                 | 30-May-25 | 31-May-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2240                                        | Resurface Pavement                                | 1                 | 02-Jun-25 | 03-Jun-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2270                                        | Reconstruct Inlets                                | 1                 | 03-Jun-25 | 04-Jun-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2250                                        | Remove Masking and Install New Pavement Markings  | 1                 | 04-Jun-25 | 05-Jun-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2260                                        | Remove Soil Erosion and Sediment Control Devices  | 1                 | 04-Jun-25 | 05-Jun-25 | 0%                  | 11          |              |               |            |            |          |           |           |             |   |   |   |   |
| STAGE 5C - HICC Multi Left Lane Closing         |                                                   |                   |           |           |                     |             |              |               |            |            |          |           |           |             |   |   |   |   |
| Pre-Stage 5C                                    |                                                   |                   |           |           |                     |             |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2290                                        | Install and Maintain MPT Devices                  | 7                 | 05-Jun-25 | 09-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2300                                        | Install Soil Erosion and Sediment Control Devices | 1                 | 05-Jun-25 | 07-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2310                                        | Close HICC Multi Left Lane                        | 1                 | 05-Jun-25 | 07-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2330                                        | Clear and Grub                                    | 1                 | 05-Jun-25 | 07-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| Stage 5C Construction                           |                                                   |                   |           |           |                     |             |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2320                                        | Removing and Masking Existing Pavement Markings   | 1                 | 07-Jun-25 | 07-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2340                                        | Install Temporary Pavement Marking Tape           | 1                 | 07-Jun-25 | 07-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2350                                        | MII Existing Pavement                             | 1                 | 07-Jun-25 | 08-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2360                                        | Resurface Pavement                                | 1                 | 08-Jun-25 | 08-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2390                                        | Reconstruct Inlets                                | 1                 | 08-Jun-25 | 08-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2370                                        | Remove Masking and Install New Pavement Markings  | 1                 | 08-Jun-25 | 09-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2380                                        | Remove Soil Erosion and Sediment Control Devices  | 1                 | 08-Jun-25 | 09-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| STAGE 5C - HICC Multi Right Lane Closing        |                                                   |                   |           |           |                     |             |              |               |            |            |          |           |           |             |   |   |   |   |
| Pre-Stage 5C                                    |                                                   |                   |           |           |                     |             |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2420                                        | Install Soil Erosion and Sediment Control Devices | 1                 | 13-Jun-25 | 14-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2430                                        | Close HICC Multi Right Lane                       | 1                 | 13-Jun-25 | 14-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2450                                        | Clear and Grub                                    | 1                 | 13-Jun-25 | 14-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2410                                        | Install and Maintain MPT Devices                  | 6                 | 14-Jun-25 | 16-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| Stage 5C Construction                           |                                                   |                   |           |           |                     |             |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2440                                        | Removing and Masking Existing Pavement Markings   | 1                 | 14-Jun-25 | 14-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2460                                        | Install Temporary Pavement Marking Tape           | 1                 | 14-Jun-25 | 14-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2470                                        | MII Existing Pavement                             | 1                 | 14-Jun-25 | 15-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2480                                        | Resurface Pavement                                | 1                 | 15-Jun-25 | 15-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2510                                        | Reconstruct Inlets                                | 1                 | 15-Jun-25 | 15-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2490                                        | Remove Masking and Install New Pavement Markings  | 1                 | 15-Jun-25 | 16-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2500                                        | Remove Soil Erosion and Sediment Control Devices  | 1                 | 15-Jun-25 | 16-Jun-25 | 0%                  | 14          |              |               |            |            |          |           |           |             |   |   |   |   |

■ Actual Work
 ■ Critical Remaining Work
 ▼ Summary
 ■ Remaining Work
 ◆ Milestone

Page 4 of 5

Work Sample

### Road Modifications

| Activity ID                                     | Activity Name                                               | Original Duration | Start     | Finish    | Schedule % Complete | Total Float | January 2025 | February 2025 | March 2025 | April 2025 | May 2025 | June 2025 | July 2025 | August 2025 | S | O | N | D |
|-------------------------------------------------|-------------------------------------------------------------|-------------------|-----------|-----------|---------------------|-------------|--------------|---------------|------------|------------|----------|-----------|-----------|-------------|---|---|---|---|
| STAGE 6 - TSO RAMP/NSO ROADWAY RIGHT SHLD. WORK |                                                             |                   |           |           |                     |             |              |               |            |            |          |           |           |             |   |   |   |   |
| Pre-Stage 6                                     |                                                             |                   |           |           |                     |             |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2540                                        | Install Soil Erosion and Sediment Control Devices           | 2                 | 16-Jun-25 | 18-Jun-25 | 0%                  | 13          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2530                                        | Install and Maintain MPT Devices                            | 34                | 16-Jun-25 | 06-Aug-25 | 0%                  | 17          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2570                                        | Clear and Grub                                              | 2                 | 18-Jun-25 | 20-Jun-25 | 0%                  | 13          |              |               |            |            |          |           |           |             |   |   |   |   |
| Stage 6 Construction                            |                                                             |                   |           |           |                     |             |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2580                                        | Removing and Masking Existing Pavement Markings             | 1                 | 20-Jun-25 | 21-Jun-25 | 0%                  | 13          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2590                                        | Install Temporary Pavement Marking Tape                     | 1                 | 20-Jun-25 | 21-Jun-25 | 0%                  | 13          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2670                                        | Remove Existing Lighting Facilities                         | 2                 | 23-Jun-25 | 25-Jun-25 | 0%                  | 13          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2690                                        | Remove Existing Guide Rail and Curb                         | 3                 | 25-Jun-25 | 28-Jun-25 | 0%                  | 13          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2610                                        | Construct Subgrade                                          | 4                 | 30-Jun-25 | 03-Jul-25 | 0%                  | 13          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2680                                        | Install Foundation and Conduits For New Lighting Facilities | 6                 | 08-Jul-25 | 17-Jul-25 | 0%                  | 13          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2620                                        | Install New Guide Rail and Concrete Curb                    | 5                 | 17-Jul-25 | 24-Jul-25 | 0%                  | 13          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2630                                        | Surface Berm                                                | 3                 | 24-Jul-25 | 29-Jul-25 | 0%                  | 13          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2690                                        | Install and Configure New Lighting Facilities               | 4                 | 29-Jul-25 | 02-Aug-25 | 0%                  | 17          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2710                                        | Remove Soil Erosion and Sediment Control Devices            | 1                 | 29-Jul-25 | 30-Jul-25 | 0%                  | 22          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2700                                        | Remove Masking and Install New Pavement Markings            | 2                 | 04-Aug-25 | 06-Aug-25 | 0%                  | 17          |              |               |            |            |          |           |           |             |   |   |   |   |
| General Site Works                              |                                                             |                   |           |           |                     |             |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2720                                        | Remove Existing Fence @ TMD-7                               | 10                | 08-May-25 | 21-May-25 | 0%                  | 52          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2730                                        | Install New Fence Improvements @ TMD-7                      | 10                | 28-May-25 | 10-Jun-25 | 0%                  | 52          |              |               |            |            |          |           |           |             |   |   |   |   |
| CON-2640                                        | Install Topsoil and Seeding                                 | 10                | 14-Aug-25 | 28-Aug-25 | 0%                  | 1           |              |               |            |            |          |           |           |             |   |   |   |   |
| Close-out                                       |                                                             |                   |           |           |                     |             |              |               |            |            |          |           |           |             |   |   |   |   |
| CL-1000                                         | Final Inspections & Punch-list                              | 7                 | 03-Sep-25 | 11-Sep-25 | 0%                  | 0           |              |               |            |            |          |           |           |             |   |   |   |   |
| CL-1010                                         | Final Clean-up & Demobilization                             | 7                 | 03-Sep-25 | 11-Sep-25 | 0%                  | 0           |              |               |            |            |          |           |           |             |   |   |   |   |

■ Actual Work
 ■ Critical Remaining Work
 ▼ Summary
 ■ Remaining Work
 ◆ Milestone

Page 5 of 5

Work Sample

## School Renovation

| Activity ID                                    | Activity Name                                                                  | Original Duration | Start     | Finish    | Schedule % Complete | Total Float |
|------------------------------------------------|--------------------------------------------------------------------------------|-------------------|-----------|-----------|---------------------|-------------|
| SA-1100                                        | Prepare & Submit General Provisions for Heating, Ventilating and Air Condition | 20                | 18-Jun-24 | 16-Jul-24 | 0%                  | 19          |
| SA-1330                                        | Review & Approve General Provisions for Heating, Ventilating and Air Condil    | 15                | 17-Jul-24 | 06-Aug-24 | 0%                  | 19          |
| Division 16 - Electrical                       |                                                                                | 35                | 18-Jun-24 | 06-Aug-24 | 0%                  | 19          |
| 16010 - General Provisions for Electrical Work |                                                                                | 35                | 18-Jun-24 | 06-Aug-24 | 0%                  | 19          |
| SA-1160                                        | Prepare & Submit General Provisions for Electrical Work                        | 20                | 18-Jun-24 | 16-Jul-24 | 0%                  | 19          |
| SA-1310                                        | Review & Approve General Provisions for Electrical Work                        | 15                | 17-Jul-24 | 06-Aug-24 | 0%                  | 19          |
| Notifications                                  |                                                                                | 1                 | 23-Aug-24 | 23-Aug-24 | 0%                  | 10          |
| NO-1010                                        | DEC Notification Letter                                                        | 1                 | 23-Aug-24 | 23-Aug-24 | 0%                  | 10          |
| Construction                                   |                                                                                | 105               | 16-Jul-24 | 15-Dec-24 | 0%                  | 0           |
| Mobilization & Site Preparation                |                                                                                | 10                | 18-Jun-24 | 23-Jul-24 | 0%                  | 0           |
| MO-1000                                        | Mobilization                                                                   | 5                 | 18-Jun-24 | 22-Jul-24 | 0%                  | 0           |
| MO-1020                                        | Remove Existing Loose Content from the Building                                | 3                 | 23-Jul-24 | 25-Jul-24 | 0%                  | 0           |
| MO-1040                                        | Install Safety Protection Measures                                             | 5                 | 23-Jul-24 | 28-Jul-24 | 0%                  | 0           |
| MO-1050                                        | Install Junction Boxes / Bypass Connections                                    | 3                 | 23-Jul-24 | 29-Jul-24 | 0%                  | 0           |
| MO-1030                                        | Install Protection to Hallway Floors                                           | 2                 | 26-Jul-24 | 29-Jul-24 | 0%                  | 0           |
| Asbestos Abatement                             |                                                                                | 82                | 30-Jul-24 | 25-Nov-24 | 0%                  | 7           |
| Asbestos Abatement at Third Floor              |                                                                                | 18                | 30-Jul-24 | 22-Aug-24 | 0%                  | 0           |
| AA-1050                                        | Electrical Cut Off - Third Floor                                               | 3                 | 30-Jul-24 | 01-Aug-24 | 0%                  | 0           |
| AA-1060                                        | Set Up of Decon Area - Third Floor                                             | 3                 | 02-Aug-24 | 06-Aug-24 | 0%                  | 0           |
| AA-1000                                        | Asbestos Abatement - Third Floor                                               | 10                | 07-Aug-24 | 20-Aug-24 | 0%                  | 0           |
| AA-1070                                        | Breakdown of Decon Area - Third Floor                                          | 2                 | 21-Aug-24 | 22-Aug-24 | 0%                  | 0           |
| Asbestos Abatement at Second Floor             |                                                                                | 18                | 23-Aug-24 | 16-Sep-24 | 0%                  | 0           |
| AA-1080                                        | Electrical Cut Off - Second Floor                                              | 3                 | 23-Aug-24 | 27-Aug-24 | 0%                  | 0           |
| AA-1090                                        | Set Up of Decon Area - Second Floor                                            | 3                 | 28-Aug-24 | 30-Aug-24 | 0%                  | 0           |
| AA-1010                                        | Asbestos Abatement - Second Floor                                              | 10                | 03-Sep-24 | 16-Sep-24 | 0%                  | 0           |
| AA-1100                                        | Breakdown of Decon Area - Second Floor                                         | 2                 | 17-Sep-24 | 18-Sep-24 | 0%                  | 0           |
| Asbestos Abatement at First Floor              |                                                                                | 18                | 15-Oct-24 | 15-Oct-24 | 0%                  | 0           |
| AA-1110                                        | Electrical Cut Off - First Floor                                               | 3                 | 15-Sep-24 | 23-Sep-24 | 0%                  | 0           |
| AA-1120                                        | Set Up of Decon Area - First Floor                                             | 3                 | 24-Sep-24 | 26-Sep-24 | 0%                  | 0           |
| AA-1020                                        | Asbestos Abatement - First Floor                                               | 10                | 27-Sep-24 | 10-Oct-24 | 0%                  | 0           |
| AA-1130                                        | Breakdown of Decon Area - First Floor                                          | 2                 | 11-Oct-24 | 15-Oct-24 | 0%                  | 0           |
| Asbestos Abatement at Basement                 |                                                                                | 18                | 16-Oct-24 | 09-Nov-24 | 0%                  | 0           |
| AA-1140                                        | Electrical Cut Off - Basement                                                  | 3                 | 16-Oct-24 | 18-Oct-24 | 0%                  | 0           |
| AA-1150                                        | Set Up of Decon Area - Basement                                                | 3                 | 21-Oct-24 | 23-Oct-24 | 0%                  | 0           |
| AA-1030                                        | Asbestos Abatement - Basement                                                  | 10                | 24-Oct-24 | 06-Nov-24 | 0%                  | 0           |
| AA-1160                                        | Breakdown of Decon Area - Basement                                             | 2                 | 07-Nov-24 | 08-Nov-24 | 0%                  | 0           |
| Asbestos Abatement at Roof                     |                                                                                | 10                | 12-Nov-24 | 25-Nov-24 | 0%                  | 7           |
| AA-1170                                        | Electrical Cut Off - Roof                                                      | 3                 | 12-Nov-24 | 14-Nov-24 | 0%                  | 7           |
| AA-1180                                        | Set Up of Decon Area - Roof                                                    | 3                 | 15-Nov-24 | 19-Nov-24 | 0%                  | 7           |
| AA-1040                                        | Asbestos Abatement - Roof                                                      | 2                 | 20-Nov-24 | 21-Nov-24 | 0%                  | 7           |
| AA-1190                                        | Breakdown of Decon Area - Roof                                                 | 2                 | 22-Nov-24 | 25-Nov-24 | 0%                  | 7           |
| Sitework - Underground Tank                    |                                                                                | 6                 | 28-Aug-24 | 03-Sep-24 | 0%                  | 11          |
| SW-1010                                        | Cleaning & Sealing Underground Tank - Sitework                                 | 4                 | 28-Aug-24 | 29-Aug-24 | 0%                  | 10          |
| SW-1020                                        | Fill Tank with Concrete Slurry - Sitework                                      | 2                 | 30-Aug-24 | 03-Sep-24 | 0%                  | 11          |
| Building Demolition Work                       |                                                                                | 77                | 23-Aug-24 | 15-Dec-24 | 0%                  | 0           |
| Demolition Work at Third Floor                 |                                                                                | 18                | 23-Aug-24 | 16-Sep-24 | 0%                  | 1           |
| Architectural Work at Third Floor              |                                                                                | 16                | 23-Aug-24 | 16-Sep-24 | 0%                  | 1           |
| DM-1090                                        | Remove Existing Wall Panel - Third Floor                                       | 3                 | 23-Aug-24 | 27-Aug-24 | 0%                  | 0           |

## School Renovation

[illegible]

### School Renovation

| Activity ID                        | Activity Name                                                           | Original Duration | Start     | Finish    | Schedule % Complete | Total Float | 2024 | June 2024 | July 2024 | August 2024 | S | October 2024 | N | D | January 2025 | F | March 2025 | 2025 |
|------------------------------------|-------------------------------------------------------------------------|-------------------|-----------|-----------|---------------------|-------------|------|-----------|-----------|-------------|---|--------------|---|---|--------------|---|------------|------|
| DM-2240                            | Remove Existing Plumbing Piping - First Floor                           | 2                 | 25-Oct-24 | 30-Oct-24 | 0%                  | 3           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2250                            | Remove Existing Plumbing Valves - First Floor                           | 2                 | 25-Oct-24 | 30-Oct-24 | 0%                  | 3           |      |           |           |             |   |              |   |   |              |   |            |      |
| <b>Demolition Work at Basement</b> |                                                                         | 18                | 08-Nov-24 | 06-Dec-24 | 0%                  | 2           |      |           |           |             |   |              |   |   |              |   |            |      |
| <b>Architectural at Basement</b>   |                                                                         | 15                | 12-Nov-24 | 04-Dec-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2310                            | Remove Existing Kitchen and Toilet Accessories - Basement               | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2360                            | Remove Existing Wall Panel - Basement                                   | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2480                            | Remove Existing Kitchen Equipments & Hood - Basement                    | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2510                            | Remove Existing Fixed Seatings - Basement                               | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2520                            | Remove Existing Metal Stair - Basement                                  | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2530                            | Remove Existing Turnstile - Basement                                    | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2540                            | Remove Existing Metal Screen & Frame - Basement                         | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2550                            | Remove Existing Locker Bench & Concrete Base - Basement                 | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2560                            | Remove Existing Handrail - Basement                                     | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2570                            | Remove Existing Wood Platform - Basement                                | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2580                            | Remove Existing Window System - Basement                                | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2320                            | Remove Existing Workstations - Basement                                 | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 2           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2330                            | Remove Existing Lockers/Metal Shelving - Basement                       | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 2           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2340                            | Remove Existing Built In Cabinet/Casework - Basement                    | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 2           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2350                            | Remove Existing Visual Display Boards - Basement                        | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 2           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2360                            | Remove Existing Millwork - Basement                                     | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 2           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2370                            | Remove Existing Accessories and Specialty Equipments - Basement         | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 2           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2430                            | Remove Existing Exit & Emergency Signs - Basement                       | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 2           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2470                            | Remove Existing Fire Extinguisher Cabinet - Basement                    | 1                 | 12-Nov-24 | 12-Nov-24 | 0%                  | 2           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2700                            | Remove Existing Cladding and Framing - Basement                         | 3                 | 14-Nov-24 | 18-Nov-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2690                            | Remove Existing Toilet Partition System - Basement                      | 2                 | 14-Nov-24 | 15-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2710                            | Remove Existing Doors and Frames - Basement                             | 2                 | 14-Nov-24 | 15-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2760                            | Remove Existing Terrazzo Floor - Basement                               | 3                 | 19-Nov-24 | 21-Nov-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2770                            | Remove Existing Carpet - Basement                                       | 2                 | 19-Nov-24 | 20-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2780                            | Remove Existing VINYL Tile Floor - Basement                             | 2                 | 19-Nov-24 | 20-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2790                            | Remove Existing Wood Floor - Basement                                   | 2                 | 19-Nov-24 | 20-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2800                            | Remove Existing Ceramic/Tiles Floor - Basement                          | 2                 | 19-Nov-24 | 20-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2820                            | Remove Existing Acoustical Ceiling System - Basement                    | 2                 | 22-Nov-24 | 25-Nov-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2850                            | Remove Existing Metal Panel Ceiling System - Basement                   | 2                 | 22-Nov-24 | 25-Nov-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2810                            | Remove Existing Plaster Cement Ceiling - Basement                       | 3                 | 22-Nov-24 | 26-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2870                            | Remove Existing Masonry Wall - Basement                                 | 3                 | 02-Dec-24 | 04-Dec-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2880                            | Remove Existing Drywall Partition and Soffit - Basement                 | 2                 | 02-Dec-24 | 03-Dec-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| <b>Mechanical at Basement</b>      |                                                                         | 14                | 08-Nov-24 | 02-Dec-24 | 0%                  | 6           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2600                            | Remove Existing Boiler Feed Tank - Basement                             | 2                 | 08-Nov-24 | 12-Nov-24 | 0%                  | 4           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2590                            | Remove Existing HVAC Equipments & Associated Piping Ductwork - Basement | 2                 | 08-Nov-24 | 12-Nov-24 | 0%                  | 5           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2380                            | Remove Existing Exhaust Collars - Basement                              | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 6           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2400                            | Remove Existing Baseboard Heater - Basement                             | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 7           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2730                            | Remove Existing Radiator Unit & Cover - Basement                        | 2                 | 14-Nov-24 | 15-Nov-24 | 0%                  | 7           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2740                            | Remove Existing Steam Convectors/Radiator - Basement                    | 2                 | 18-Nov-24 | 19-Nov-24 | 0%                  | 7           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2860                            | Remove Existing Exhaust Fan - Basement                                  | 2                 | 26-Nov-24 | 27-Nov-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-3080                            | Remove Existing HVAC Ductwork & Piping - Basement                       | 2                 | 27-Nov-24 | 02-Dec-24 | 0%                  | 6           |      |           |           |             |   |              |   |   |              |   |            |      |
| <b>Electrical at Basement</b>      |                                                                         | 17                | 12-Nov-24 | 06-Dec-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2670                            | Remove Existing Water Tank Electrical Connections - Basement            | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 3           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2420                            | Remove Existing Light Fixtures - Basement                               | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 6           |      |           |           |             |   |              |   |   |              |   |            |      |

■ Actual Work
 ■ Critical Remaining Work
 ■ Summary
 ■ Remaining Work
 ◆ Milestone

Page 7 of 9

Work Sample

### School Renovation

| Activity ID                                                   | Activity Name                                                            | Original Duration | Start     | Finish    | Schedule % Complete | Total Float | 2024 | June 2024 | July 2024 | August 2024 | S | October 2024 | N | D | January 2025 | F | March 2025 | 2025 |
|---------------------------------------------------------------|--------------------------------------------------------------------------|-------------------|-----------|-----------|---------------------|-------------|------|-----------|-----------|-------------|---|--------------|---|---|--------------|---|------------|------|
| DM-2410                                                       | Remove Existing Receptacles - Basement                                   | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 7           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2500                                                       | Remove Existing Dimmer Board - Basement                                  | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 11          |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2610                                                       | Remove Existing Circuit Breaker - Basement                               | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 11          |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2620                                                       | Remove Existing Score Screen - Basement                                  | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 11          |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2630                                                       | Remove Existing Cameras - Basement                                       | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 11          |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2640                                                       | Remove Existing Speaker - Basement                                       | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 11          |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2650                                                       | Remove Existing Sound Rack - Basement                                    | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 11          |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2660                                                       | Remove Existing Outdoor Intercom Calling Push Button - Basement          | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 11          |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2720                                                       | Remove Existing Electrical Panel - Basement                              | 2                 | 14-Nov-24 | 15-Nov-24 | 0%                  | 7           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2750                                                       | Remove Existing Junction Box & Power Connections - Basement              | 2                 | 18-Nov-24 | 19-Nov-24 | 0%                  | 7           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-3050                                                       | Remove Existing Electrical Rough-ins - Basement                          | 2                 | 05-Dec-24 | 06-Dec-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2890                                                       | Remove Existing Fire Alarm System - Basement                             | 1                 | 05-Dec-24 | 05-Dec-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| <b>Plumbing at Basement</b>                                   |                                                                          | 9                 | 12-Nov-24 | 22-Nov-24 | 0%                  | 4           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2440                                                       | Remove Existing Plumbing Fixtures - Basement                             | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2450                                                       | Remove Existing Water & Gas Risers - Basement                            | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2460                                                       | Remove Existing Floor Drain Cover - Basement                             | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 4           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2880                                                       | Remove Plumbing Equipments - Basement                                    | 2                 | 12-Nov-24 | 13-Nov-24 | 0%                  | 9           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2830                                                       | Remove Existing Plumbing Piping - Basement                               | 2                 | 21-Nov-24 | 22-Nov-24 | 0%                  | 4           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2840                                                       | Remove Existing Plumbing Valves - Basement                               | 2                 | 21-Nov-24 | 22-Nov-24 | 0%                  | 4           |      |           |           |             |   |              |   |   |              |   |            |      |
| <b>Demolition Work at Roof</b>                                |                                                                          | 6                 | 09-Dec-24 | 15-Dec-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| <b>Architectural at Roof</b>                                  |                                                                          | 2                 | 13-Dec-24 | 15-Dec-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-3010                                                       | Remove Existing Roof Cuts - Roof                                         | 2                 | 13-Dec-24 | 15-Dec-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| <b>Mechanical at Roof</b>                                     |                                                                          | 5                 | 09-Dec-24 | 12-Dec-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2930                                                       | Remove Existing HVAC Equipment & Associated Piping Ductwork - Roof       | 4                 | 09-Dec-24 | 12-Dec-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2970                                                       | Remove Existing Radiator Unit & Cover - Roof                             | 4                 | 09-Dec-24 | 12-Dec-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2900                                                       | Remove Existing Steam Convectors - Roof                                  | 4                 | 09-Dec-24 | 12-Dec-24 | 0%                  | 2           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2910                                                       | Remove Existing Outdoor Condensing Units - Roof                          | 4                 | 09-Dec-24 | 12-Dec-24 | 0%                  | 2           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2920                                                       | Remove Existing Exhaust Fan - Roof                                       | 4                 | 09-Dec-24 | 12-Dec-24 | 0%                  | 2           |      |           |           |             |   |              |   |   |              |   |            |      |
| <b>Electrical at Roof</b>                                     |                                                                          | 5                 | 09-Dec-24 | 13-Dec-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2940                                                       | Remove Existing Electrical Panel - Roof                                  | 5                 | 09-Dec-24 | 13-Dec-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2950                                                       | Remove Existing Light Fixtures - Roof                                    | 5                 | 09-Dec-24 | 13-Dec-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2980                                                       | Remove Existing Fire Alarm System - Roof                                 | 5                 | 09-Dec-24 | 13-Dec-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-3000                                                       | Remove Existing Electrical Services Light, Power, and Low Voltage - Roof | 5                 | 09-Dec-24 | 13-Dec-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2990                                                       | Remove Existing Power for Elevator - Roof                                | 2                 | 09-Dec-24 | 10-Dec-24 | 0%                  | 4           |      |           |           |             |   |              |   |   |              |   |            |      |
| <b>Plumbing at Roof</b>                                       |                                                                          | 5                 | 09-Dec-24 | 13-Dec-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-3090                                                       | Provide Watertight Seal - Roof                                           | 2                 | 09-Dec-24 | 10-Dec-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| DM-2960                                                       | Remove Existing Plumbing Vents - Roof                                    | 3                 | 11-Dec-24 | 13-Dec-24 | 0%                  | 1           |      |           |           |             |   |              |   |   |              |   |            |      |
| <b>Close-Out Submittals</b>                                   |                                                                          | 59                | 27-Jun-24 | 19-Sep-24 | 0%                  | 11          |      |           |           |             |   |              |   |   |              |   |            |      |
| NO-1000                                                       | PWN for Closure of Tanks                                                 | 1                 | 27-Jun-24 | 27-Jun-24 | 0%                  | 74          |      |           |           |             |   |              |   |   |              |   |            |      |
| SA-1350                                                       | Prepare & Submit Tank Closure Report                                     | 21                | 30-Aug-24 | 19-Sep-24 | 0%                  | 17          |      |           |           |             |   |              |   |   |              |   |            |      |
| SA-1340                                                       | Prepare & Submit Tank Closure Affidavit                                  | 14                | 30-Aug-24 | 12-Sep-24 | 0%                  | 24          |      |           |           |             |   |              |   |   |              |   |            |      |
| <b>0215 - Petroleum Bulk Storage Tank System Closure Plan</b> |                                                                          | 35                | 27-Jun-24 | 15-Aug-24 | 0%                  | 18          |      |           |           |             |   |              |   |   |              |   |            |      |
| SA-1130                                                       | Prepare & Submit Petroleum Bulk Storage Tank System Closure Plan         | 20                | 27-Jun-24 | 25-Jul-24 | 0%                  | 16          |      |           |           |             |   |              |   |   |              |   |            |      |
| SA-1280                                                       | Review & Approve Petroleum Bulk Storage Tank System Closure Plan         | 15                | 28-Jul-24 | 15-Aug-24 | 0%                  | 16          |      |           |           |             |   |              |   |   |              |   |            |      |
| <b>Close-Out</b>                                              |                                                                          | 20                | 18-Dec-24 | 14-Jan-25 | 0%                  | 8           |      |           |           |             |   |              |   |   |              |   |            |      |
| CO-1000                                                       | Pre-Final Inspection                                                     | 6                 | 18-Dec-24 | 23-Dec-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| CO-1040                                                       | Construction Inspection Division (CID)                                   | 6                 | 18-Dec-24 | 23-Dec-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |
| CO-1010                                                       | Punchlist                                                                | 5                 | 24-Dec-24 | 31-Dec-24 | 0%                  | 0           |      |           |           |             |   |              |   |   |              |   |            |      |

■ Actual Work
 ■ Critical Remaining Work
 ■ Summary
 ■ Remaining Work
 ◆ Milestone

Page 8 of 9

Work Sample

## Security Enhancements

| Activity ID                                    | Activity Name                                                                | Original Duration | Start     | Finish    | Schedule % Complete | Total Float | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O |
|------------------------------------------------|------------------------------------------------------------------------------|-------------------|-----------|-----------|---------------------|-------------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| PC-1620                                        | R&A Shop Drawings - Risers                                                   | 14                | 29-Jul-25 | 15-Aug-25 | 0%                  | 12          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| PC-1430                                        | R&A Shop Drawings - Fifth Floor                                              | 14                | 05-Aug-25 | 22-Aug-25 | 0%                  | 27          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| PC-1450                                        | R&A Shop Drawings - Second Floor                                             | 14                | 12-Aug-25 | 29-Aug-25 | 0%                  | 48          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| PC-1460                                        | R&A Shop Drawings - Third Floor                                              | 14                | 19-Aug-25 | 08-Sep-25 | 0%                  | 120         |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| PC-1470                                        | R&A Shop Drawings - Fourth Floor                                             | 14                | 26-Aug-25 | 15-Sep-25 | 0%                  | 69          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| PC-1480                                        | R&A Shop Drawings - Sixth Floor                                              | 14                | 03-Sep-25 | 22-Sep-25 | 0%                  | 135         |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| PC-1490                                        | R&A Shop Drawings - Roof & Rear                                              | 14                | 10-Sep-25 | 29-Sep-25 | 0%                  | 77          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| PC-1440                                        | R&A Shop Drawings - First Floor                                              | 14                | 24-Sep-25 | 14-Oct-25 | 0%                  | 87          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| PC-1500                                        | R&A Shop Drawings - Ceiling                                                  | 14                | 08-Oct-25 | 28-Oct-25 | 0%                  | 121         |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Construction</b>                            |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Mobilization</b>                            |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| MO-1010                                        | Mobilization                                                                 | 2                 | 02-Sep-25 | 03-Sep-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Construction</b>                            |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>General Works</b>                           |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1020                                       | Install Best Resistant Window Film on Interior Side on All Floors            | 20                | 04-Sep-25 | 01-Oct-25 | 0%                  | 172         |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Risers</b>                                  |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1850                                       | Install Riser Feeder - Electrical                                            | 10                | 04-Sep-25 | 17-Sep-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1860                                       | Install Riser Feeder - Communication                                         | 10                | 18-Sep-25 | 01-Oct-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Fifth Floor</b>                             |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Fifth Floor - Demolition</b>                |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1570                                       | Safety and Security Demolition - 5th Floor                                   | 1                 | 02-Oct-25 | 02-Oct-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Fifth Floor - Construction</b>              |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Fifth Floor - Safety and Security Work</b>  |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1580                                       | Install Cameras, Access Control Devices & Other Security Devices - 5th Floor | 6                 | 03-Oct-25 | 10-Oct-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1610                                       | Install Conduit/Wires - 5th Floor                                            | 8                 | 14-Oct-25 | 23-Oct-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1620                                       | Install Patch Panel & Terminations - 5th Floor                               | 2                 | 24-Oct-25 | 27-Oct-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1630                                       | Install Communication Cabinet - 5th Floor                                    | 2                 | 28-Oct-25 | 29-Oct-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1640                                       | Install Security Panel - 5th Floor                                           | 2                 | 30-Oct-25 | 31-Oct-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Fifth Floor - Electrical Work</b>           |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1220                                       | Install Electrical Panel and Associated Wiring - 5th Floor                   | 1                 | 03-Oct-25 | 03-Oct-25 | 0%                  | 14          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1840                                       | Install Conduit/Wires - 5th Floor                                            | 5                 | 06-Oct-25 | 10-Oct-25 | 0%                  | 14          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Fifth Floor - Testing</b>                   |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1650                                       | Testing and Commissioning Systems - 5th Floor                                | 5                 | 03-Nov-25 | 07-Nov-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Second Floor</b>                            |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Second Floor - Demolition</b>               |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1360                                       | Safety and Security Demolition - 2nd Floor                                   | 2                 | 16-Nov-25 | 12-Nov-25 | 0%                  | 24          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1120                                       | Architectural Demolition - 2nd Floor                                         | 2                 | 16-Nov-25 | 12-Nov-25 | 0%                  | 24          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Second Floor - Construction</b>             |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Second Floor - Safety and Security Work</b> |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1370                                       | Install Cameras, Access Control Devices & Other Security Devices - 2nd Floor | 8                 | 13-Nov-25 | 24-Nov-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1400                                       | Install Conduit/Wires - 2nd Floor                                            | 11                | 25-Nov-25 | 11-Dec-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1410                                       | Install Patch Panel & Terminations - 2nd Floor                               | 1                 | 12-Dec-25 | 12-Dec-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1420                                       | Install Communication Cabinet - 2nd Floor                                    | 2                 | 16-Dec-25 | 16-Dec-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1430                                       | Install Security Panel - 2nd Floor                                           | 2                 | 17-Dec-25 | 18-Dec-25 | 0%                  | 0           |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Second Floor - Architectural</b>            |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1150                                       | Install H.M. Doors and Frames - 2nd Floor                                    | 2                 | 10-Nov-25 | 12-Nov-25 | 0%                  | 24          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| <b>Second Floor - Electrical Work</b>          |                                                                              |                   |           |           |                     |             |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
| CON-1140                                       | Install UPS-3 - 2nd Floor                                                    | 1                 | 13-Nov-25 | 13-Nov-25 | 0%                  | 19          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |


Page 2 of 4

Work Sample


## Security Enhancements



| Activity ID                                    | Activity Name                                                               | Original Duration | Start     | Finish    | Schedule % Complete | Total Float |
|------------------------------------------------|-----------------------------------------------------------------------------|-------------------|-----------|-----------|---------------------|-------------|
| C0N-1160                                       | Install Electrical Panel and Associated Wiring - 2nd Floor                  | 1                 | 14-Nov-25 | 14-Nov-25 | 0%                  | 19          |
| C0N-1180                                       | Install Conduits - 2nd Floor                                                | 3                 | 17-Jan-26 | 19-Nov-25 | 0%                  | 19          |
| <b>Second Floor - Testing</b>                  |                                                                             | 5                 | 19-Dec-25 | 26-Dec-25 | 0%                  | 0           |
| C0N-1440                                       | Testing and Commissioning Systems - 2nd Floor                               | 5                 | 19-Dec-25 | 26-Dec-25 | 0%                  | 0           |
| <b>Third Floor</b>                             |                                                                             | 25                | 10-Nov-25 | 17-Dec-25 | 0%                  | 77          |
| <b>Third Floor - Demolition</b>                |                                                                             | 3                 | 10-Nov-25 | 13-Nov-25 | 0%                  | 77          |
| C0N-1450                                       | Safety and Security Demolition-3rd Floor                                    | 3                 | 10-Nov-25 | 13-Nov-25 | 0%                  | 77          |
| <b>Third Floor - Construction</b>              |                                                                             | 22                | 14-Nov-25 | 17-Dec-25 | 0%                  | 77          |
| <b>Third Floor - Safety and Security Work</b>  |                                                                             | 19                | 14-Nov-25 | 12-Dec-25 | 0%                  | 77          |
| C0N-1460                                       | Install Cameras, Access Control Devices & Other Security Devices - 3rd Floo | 8                 | 14-Nov-25 | 25-Nov-25 | 0%                  | 77          |
| C0N-1490                                       | Install Conduit/Wires - 3rd Floor                                           | 11                | 26-Nov-25 | 12-Dec-25 | 0%                  | 77          |
| <b>Third Floor - Testing</b>                   |                                                                             | 3                 | 15-Dec-25 | 17-Dec-25 | 0%                  | 77          |
| C0N-1500                                       | Testing and Commissioning Systems - 3rd Floor                               | 3                 | 15-Dec-25 | 17-Dec-25 | 0%                  | 77          |
| <b>Fourth Floor</b>                            |                                                                             | 16                | 24-Dec-25 | 23-Jan-26 | 0%                  | 0           |
| <b>Fourth Floor - Demolition</b>               |                                                                             | 1                 | 28-Dec-25 | 29-Dec-25 | 0%                  | 0           |
| C0N-1510                                       | Safety and Security Demolition - 4th Floor                                  | 1                 | 28-Dec-25 | 29-Dec-25 | 0%                  | 0           |
| <b>Fourth Floor - Construction</b>             |                                                                             | 17                | 30-Dec-25 | 23-Jan-26 | 0%                  | 0           |
| <b>Fourth Floor - Safety and Security Work</b> |                                                                             | 14                | 30-Dec-25 | 20-Jan-26 | 0%                  | 0           |
| C0N-1520                                       | Install Cameras, Access Control Devices & Other Security Devices - 4th Floo | 6                 | 30-Dec-25 | 07-Jan-26 | 0%                  | 0           |
| C0N-1550                                       | Install Conduit/Wires - 4th Floor                                           | 8                 | 08-Jan-26 | 20-Jan-26 | 0%                  | 0           |
| <b>Fourth Floor - Testing</b>                  |                                                                             | 3                 | 21-Jan-26 | 23-Jan-26 | 0%                  | 0           |
| C0N-1560                                       | Testing and Commissioning Systems - 4th Floor                               | 3                 | 21-Jan-26 | 23-Jan-26 | 0%                  | 0           |
| <b>Sixth Floor</b>                             |                                                                             | 24                | 18-Dec-25 | 23-Jan-26 | 0%                  | 77          |
| <b>Sixth Floor - Demolition</b>                |                                                                             | 3                 | 19-Dec-25 | 22-Dec-25 | 0%                  | 77          |
| C0N-1660                                       | Safety and Security Demolition - 6th Floor                                  | 3                 | 19-Dec-25 | 22-Dec-25 | 0%                  | 77          |
| <b>Sixth Floor - Construction</b>              |                                                                             | 21                | 22-Dec-25 | 23-Jan-26 | 0%                  | 77          |
| <b>Sixth Floor - Safety and Security Work</b>  |                                                                             | 16                | 24-Dec-25 | 19-Jan-26 | 0%                  | 77          |
| C0N-1670                                       | Install Cameras, Access Control Devices & Other Security Devices - 6th Floo | 6                 | 24-Dec-25 | 31-Dec-25 | 0%                  | 77          |
| C0N-1700                                       | Install Conduit/Wires - 6th Floor                                           | 8                 | 02-Jan-26 | 13-Jan-26 | 0%                  | 77          |
| C0N-1710                                       | Install Communication Cabinet - 6th Floor                                   | 2                 | 14-Jan-26 | 15-Jan-26 | 0%                  | 77          |
| <b>Sixth Floor - Testing</b>                   |                                                                             | 5                 | 16-Jan-26 | 23-Jan-26 | 0%                  | 77          |
| C0N-1720                                       | Testing and Commissioning Systems - 6th Floor                               | 5                 | 16-Jan-26 | 23-Jan-26 | 0%                  | 77          |
| <b>Roof</b>                                    |                                                                             | 20                | 26-Jan-26 | 29-Feb-26 | 0%                  | 0           |
| <b>Roof - Demolition</b>                       |                                                                             | 3                 | 26-Jan-26 | 28-Jan-26 | 0%                  | 13          |
| C0N-1730                                       | Safety and Security Demolition - Roof                                       | 1                 | 26-Jan-26 | 26-Jan-26 | 0%                  | 0           |
| C0N-1200                                       | Architectural Demolition - Roof                                             | 3                 | 26-Jan-26 | 28-Jan-26 | 0%                  | 13          |
| <b>Roof - Construction</b>                     |                                                                             | 20                | 26-Jan-26 | 29-Feb-26 | 0%                  | 0           |
| <b>Roof - Safety and Security Work</b>         |                                                                             | 15                | 27-Jan-26 | 13-Feb-26 | 0%                  | 0           |
| C0N-1740                                       | Install Cameras, Access Control Devices & Other Security Devices - Roof     | 5                 | 27-Jan-26 | 01-Feb-26 | 0%                  | 0           |
| C0N-1770                                       | Install Conduit/Wires - Roof                                                | 10                | 02-Feb-26 | 13-Feb-26 | 0%                  | 0           |
| <b>Roof - Architectural</b>                    |                                                                             | 3                 | 26-Jan-26 | 28-Jan-26 | 0%                  | 13          |
| C0N-1210                                       | Install H.M. Doors and Frames for All Doors - Roof                          | 3                 | 26-Jan-26 | 28-Jan-26 | 0%                  | 13          |
| <b>Roof - Testing</b>                          |                                                                             | 4                 | 17-Feb-26 | 20-Feb-26 | 0%                  | 0           |
| C0N-1780                                       | Testing and Commissioning Systems - Roof                                    | 4                 | 17-Feb-26 | 20-Feb-26 | 0%                  | 0           |
| <b>Rear Entrance</b>                           |                                                                             | 23                | 26-Jan-26 | 27-Feb-26 | 0%                  | 77          |
| <b>Rear Entrance - Construction</b>            |                                                                             | 20                | 26-Jan-26 | 27-Feb-26 | 0%                  | 77          |
| <b>Rear Entrance - Architectural</b>           |                                                                             | 9                 | 26-Jan-26 | 04-Feb-26 | 0%                  | 77          |
| C0N-1240                                       | Remove Existing Fence - Rear Entrance                                       | 3                 | 26-Jan-26 | 28-Jan-26 | 0%                  | 77          |



## Security Enhancements

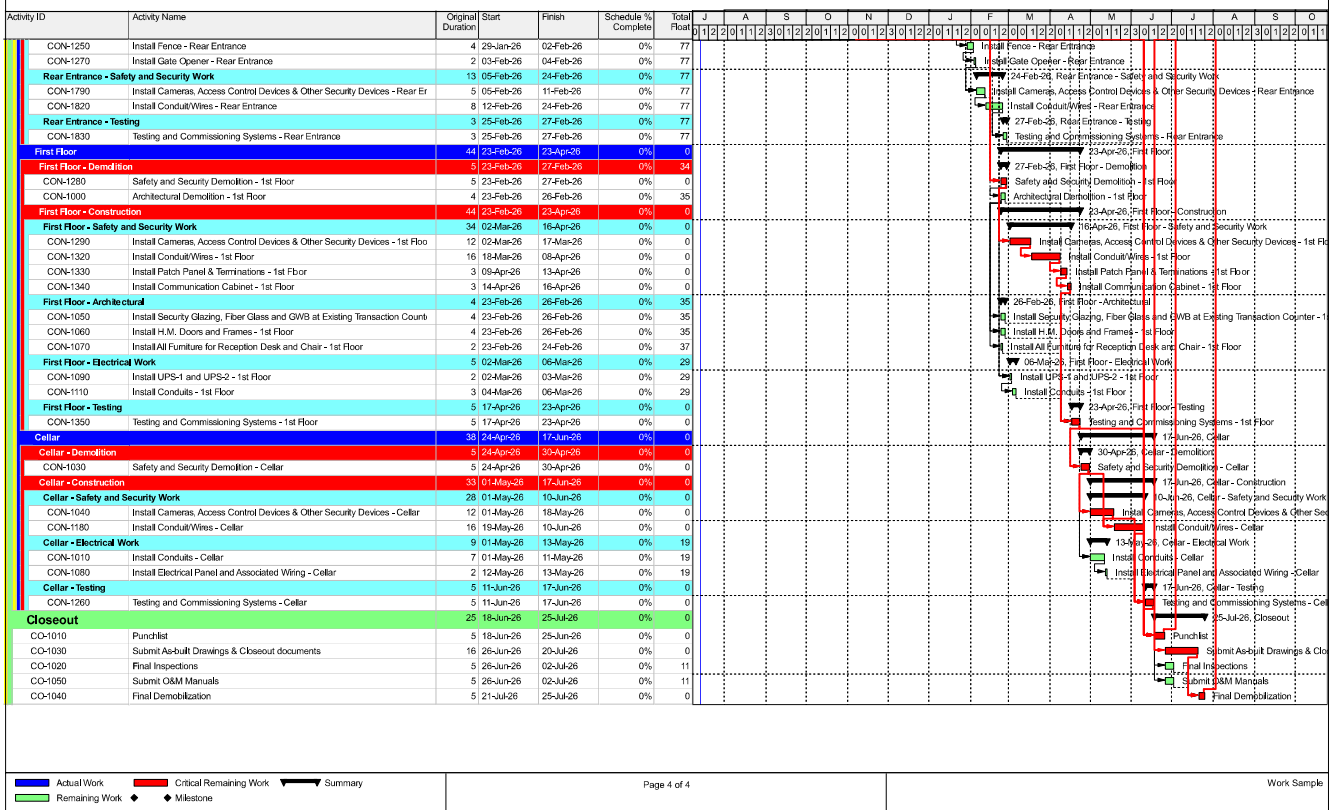

## Subway Station Renovations

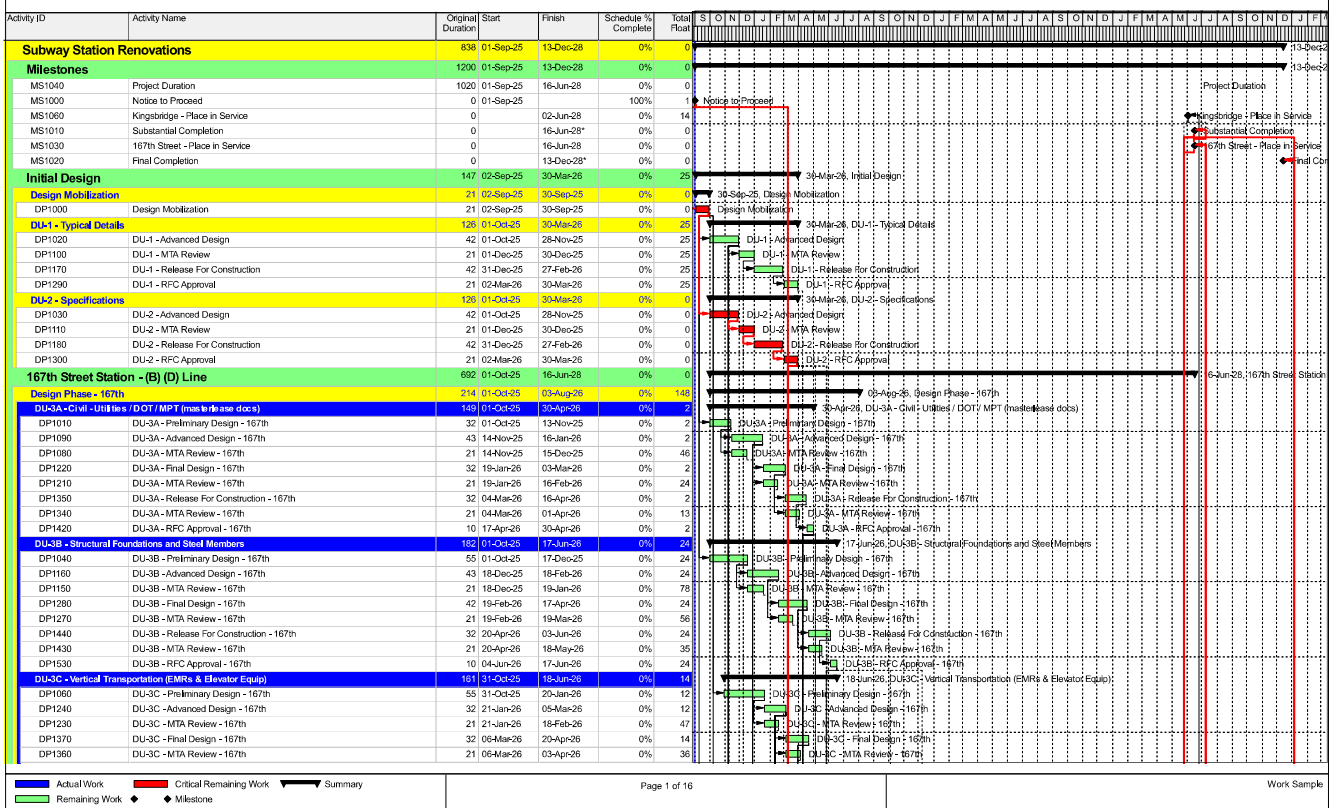

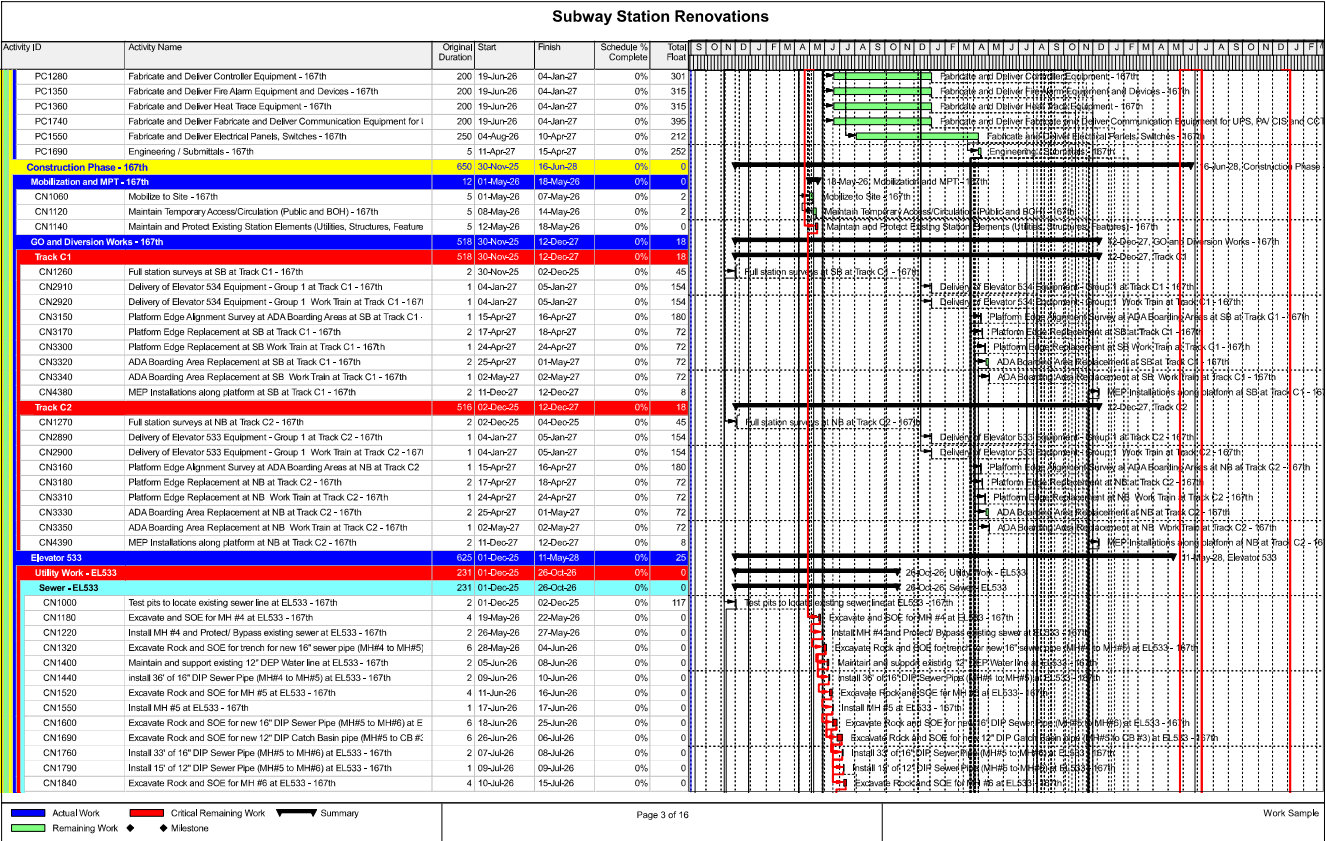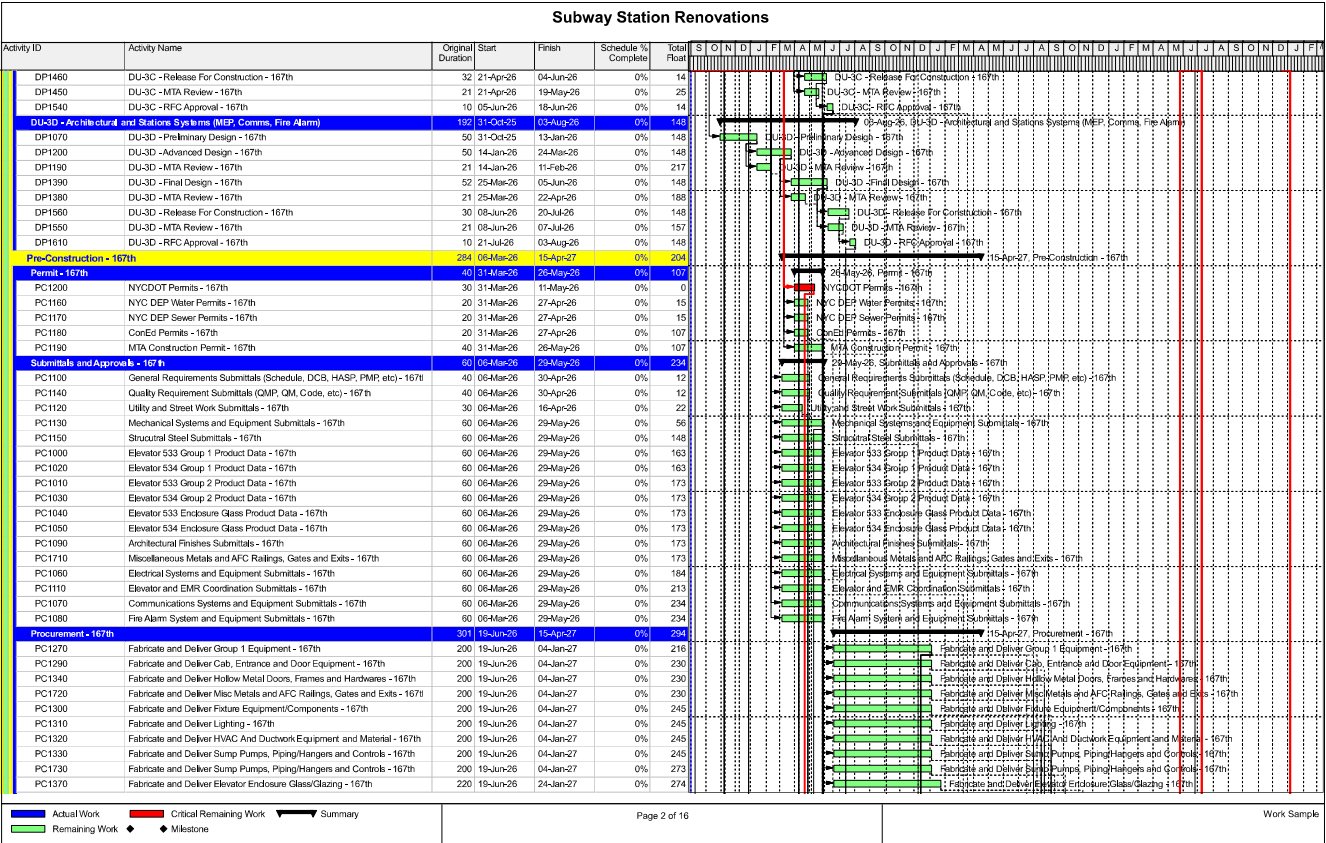


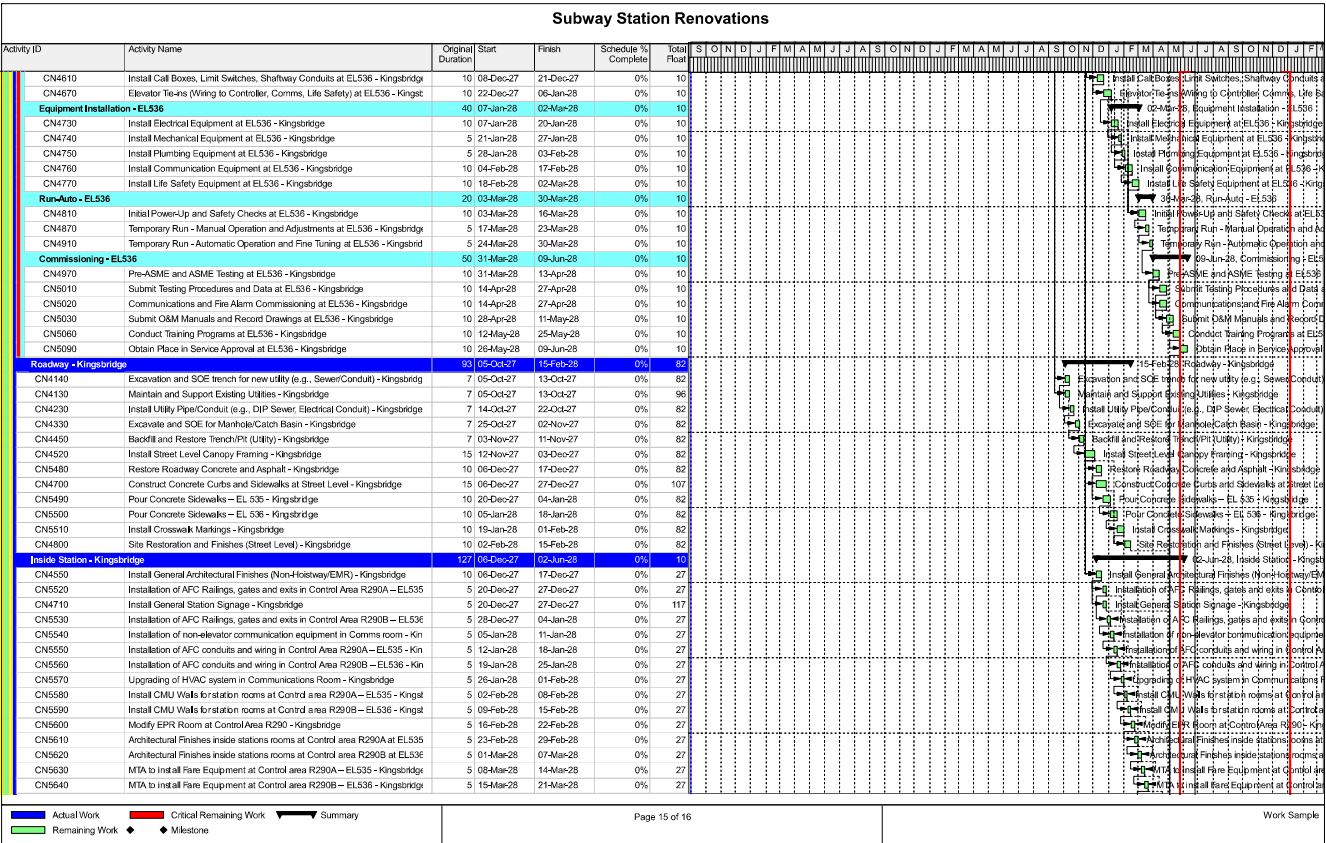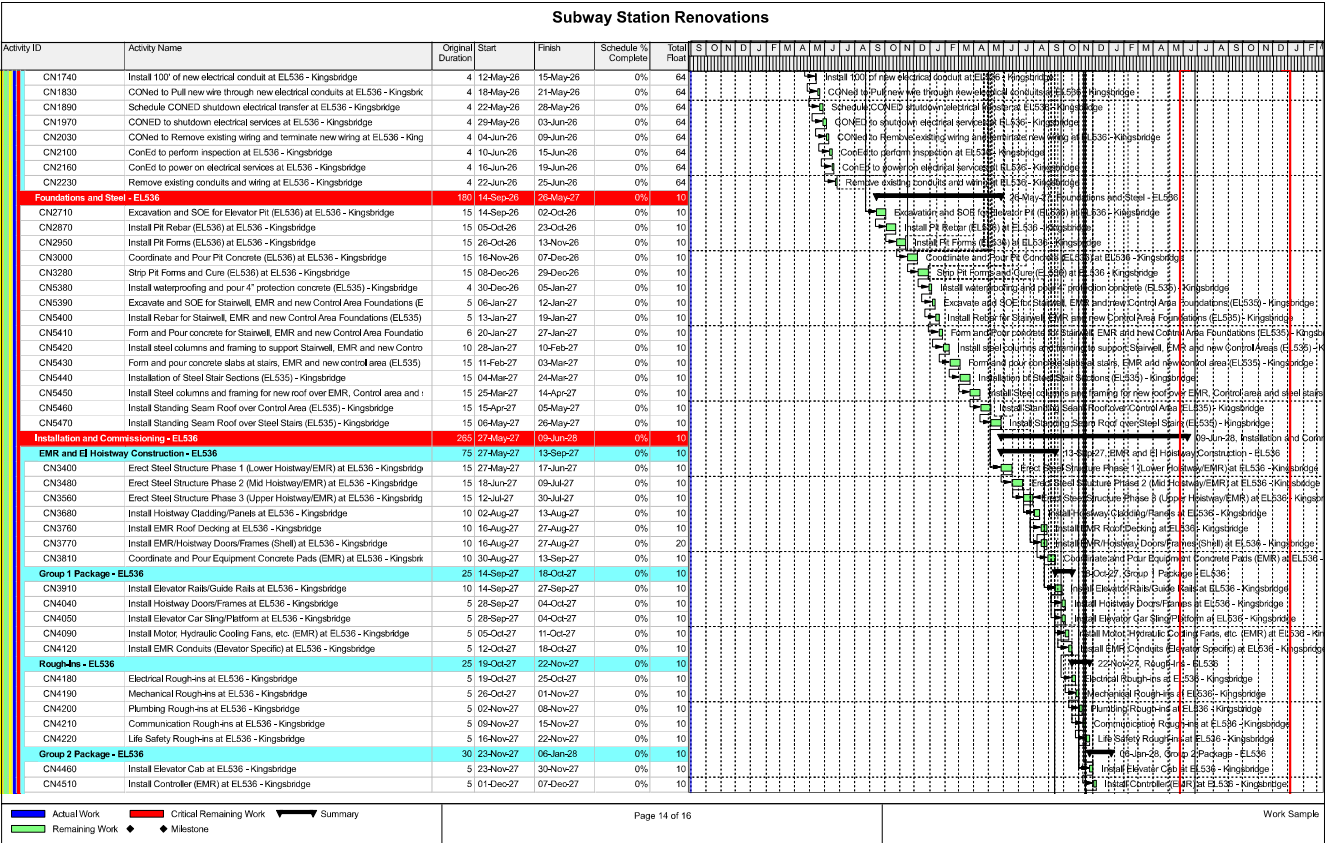

|                 |                                                                             |                   |           |           |                     |             | <h3 style="text-align: center;">Subway Station Renovations</h3>                                                                                                                                                                                                                                                                                                                                                                                         |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|-----------------|-----------------------------------------------------------------------------|-------------------|-----------|-----------|---------------------|-------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
| Activity ID     | Activity Name                                                               | Original Duration | Start     | Finish    | Schedule % Complete | Total Float | S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F                                                                                                                                                                                                                                                                                                                                                                     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| CN5650          | Installation of MEP conduits, piping and equipment for Control Area R290A   | 5                 | 22-Mar-28 | 28-Mar-28 | 0%                  | 27          | <p>Detailed Gantt Chart Description:<br/>The chart displays activities across months from March to December 2028.<br/><b>Actual Work:</b> Solid blue bars.<br/><b>Milestones:</b> Diamond shapes.<br/><b>Critical Remaining Work:</b> Red outline boxes.<br/><b>Summary:</b> Black arrows indicating duration.<br/>Key events include the completion of various installation tasks by April-May 2028, followed by closeout phases starting in June.</p> |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| CN5660          | Installation of MEP conduits, piping and equipment for Control Area R290B   | 5                 | 29-Mar-28 | 04-Apr-28 | 0%                  | 27          |                                                                                                                                                                                                                                                                                                                                                                                                                                                         |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| CN5670          | Install all Stair railings \$5/M/P10 – EL535 - Kingsbridge                  | 5                 | 05-Apr-28 | 11-Apr-28 | 0%                  | 27          |                                                                                                                                                                                                                                                                                                                                                                                                                                                         |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| CN5680          | Install all Stair railings \$5/M/P9 – EL535 - Kingsbridge                   | 5                 | 12-Apr-28 | 18-Apr-28 | 0%                  | 27          |                                                                                                                                                                                                                                                                                                                                                                                                                                                         |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| CN5690          | Installation of wind screen around Control Area R290A – EL535 - Kingsbridg  | 5                 | 19-Apr-28 | 25-Apr-28 | 0%                  | 27          |                                                                                                                                                                                                                                                                                                                                                                                                                                                         |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| CN5700          | Installation of wind screen around Control Area R290A – EL535 - Kingsbridge | 5                 | 26-Apr-28 | 02-May-28 | 0%                  | 27          |                                                                                                                                                                                                                                                                                                                                                                                                                                                         |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| CN5110          | Final Site Cleanup - Kingsbridge                                            | 5                 | 26-May-28 | 02-Jun-28 | 0%                  | 10          |                                                                                                                                                                                                                                                                                                                                                                                                                                                         |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Closeout</b> |                                                                             | 180               | 17-Jun-28 | 13-Dec-28 | 0%                  | 0           |                                                                                                                                                                                                                                                                                                                                                                                                                                                         |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| CO1000          | 167th Street - Close-out                                                    | 180               | 17-Jun-28 | 13-Dec-28 | 0%                  | 0           |                                                                                                                                                                                                                                                                                                                                                                                                                                                         |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| CO1050          | Kingsbridge - Close-out                                                     | 180               | 17-Jun-28 | 13-Dec-28 | 0%                  | 0           |                                                                                                                                                                                                                                                                                                                                                                                                                                                         |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |

**█ Actual Work**    
 **▭ Critical Remaining Work**    
 → Summary  
**▬ Remaining Work**    
 ◆ Milestone

Page 16 of 16
Work Sample

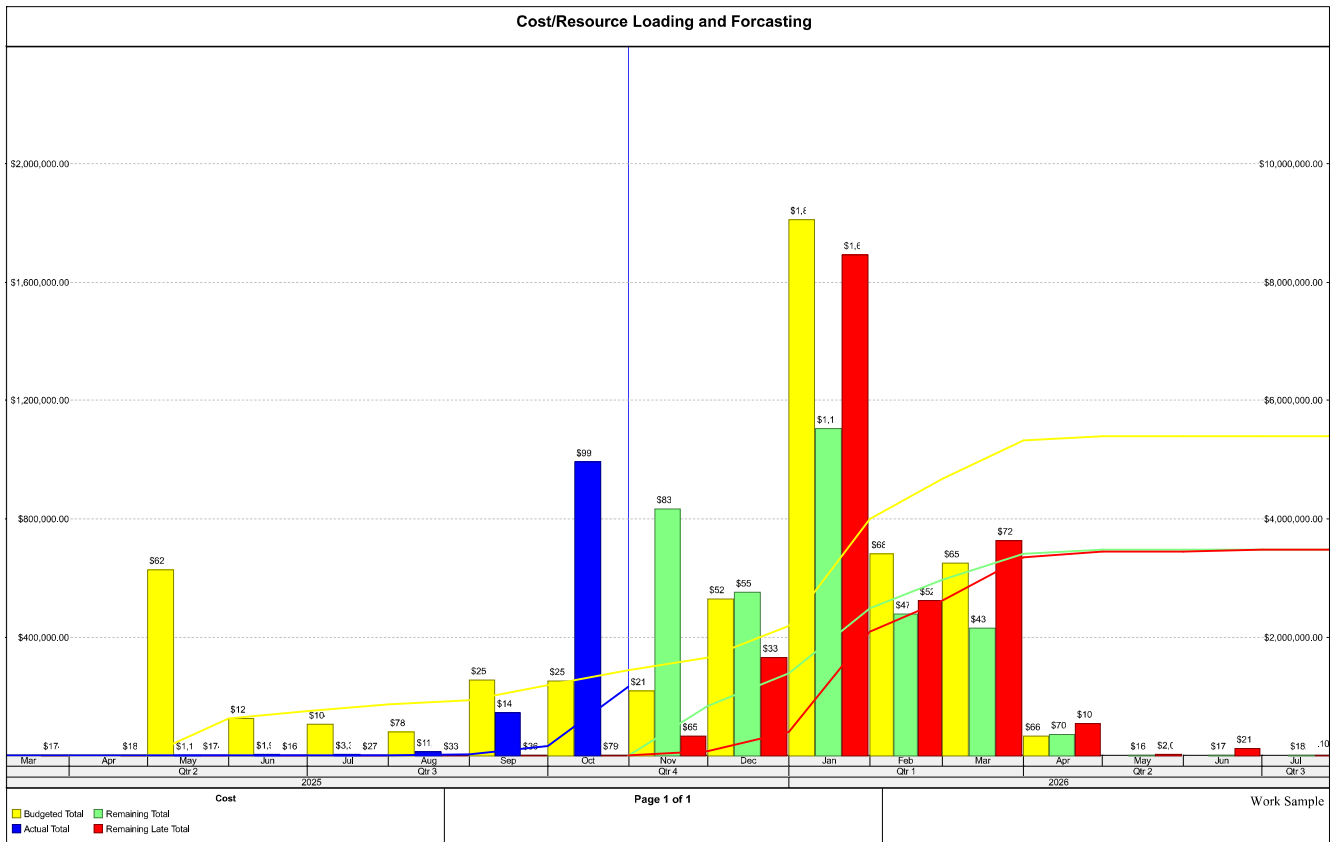

# Life Cycle Assessment of Two Asphalt Mixes – Asphalt Mix 1

## Inputs/Outputs - Raw Material Production

| Inputs            |                      |         |      |            |             |           |                                 |           |       |  |
|-------------------|----------------------|---------|------|------------|-------------|-----------|---------------------------------|-----------|-------|--|
| Flow              | Category             | Amount  | Unit | Costs/R... | Uncertai... | Avoide... | Provider                        | Data q... | Locat |  |
| Basalt (ground)   | Materials product... | 0.89000 | t    |            | none        |           | Basalt grinding, productio...   |           |       |  |
| Bitumen           | Materials product... | 0.05000 | t    |            | none        |           | Bitumen at refinery, produ...   |           |       |  |
| Quartz sand (0/2) | Materials product... | 0.06000 | t    |            | none        |           | Quartz/Silica sand, single r... |           |       |  |

## Inputs/Outputs - Transport mix materials

| Inputs    |                      |          |      |            |             |           |          |           |          |            |
|-----------|----------------------|----------|------|------------|-------------|-----------|----------|-----------|----------|------------|
| Flow      | Category             | Amount   | Unit | Costs/R... | Uncertai... | Avoide... | Provider | Data q... | Location | Descrip... |
| Transport | Materials product... | 6.00000  | tkm  |            | none        |           | Arti...  |           |          |            |
| Transport | Materials product... | 89.00000 | tkm  |            | none        |           | Arti...  |           |          |            |
| Transport | Materials product... | 10.00000 | tkm  |            | none        |           | Arti...  |           |          |            |

## Inputs/Outputs - Asphalt plant operation


| Inputs           |                       |           |      |            |             |           |          |           |          |            |
|------------------|-----------------------|-----------|------|------------|-------------|-----------|----------|-----------|----------|------------|
| Flow             | Category              | Amount    | Unit | Costs/R... | Uncertai... | Avoide... | Provider | Data q... | Location | Descrip... |
| Diesel consum... | Materials product...  | 1.12000   | kg   |            | none        |           | Die...   |           |          |            |
| Electricity      | Energy carriers an... | 30.00000  | MJ   |            | none        |           | Elec...  |           |          |            |
| Thermal energ... | Energy carriers an... | 330.00... | MJ   |            | none        |           | The...   |           |          |            |

## Inputs/Outputs - Asphalt mix

| Inputs                        |          |           |      |                |             |               |             |                 |          |            |
|-------------------------------|----------|-----------|------|----------------|-------------|---------------|-------------|-----------------|----------|------------|
| Flow                          | Category | Amount    | Unit | Costs/Reven... | Uncertainty | Avoided wa... | Provider    | Data quality... | Location | Descrip... |
| Material Manufactured         |          | 1.00000   | t    |                | none        |               | Asphalt ... |                 |          |            |
| Material transported to plant |          | 105.00000 | tkm  |                | none        |               | Material... |                 |          |            |
| Raw Material                  |          | 1.00000   | t    |                | none        |               | Raw Mat...  |                 |          |            |

| Outputs     |          |         |      |                |             |               |          |                 |          |             |
|-------------|----------|---------|------|----------------|-------------|---------------|----------|-----------------|----------|-------------|
| Flow        | Category | Amount  | Unit | Costs/Reven... | Uncertainty | Avoided pr... | Provider | Data quality... | Location | Description |
| Asphalt mix |          | 1.00000 | t    |                | none        |               |          |                 |          |             |

Impact category Climate change

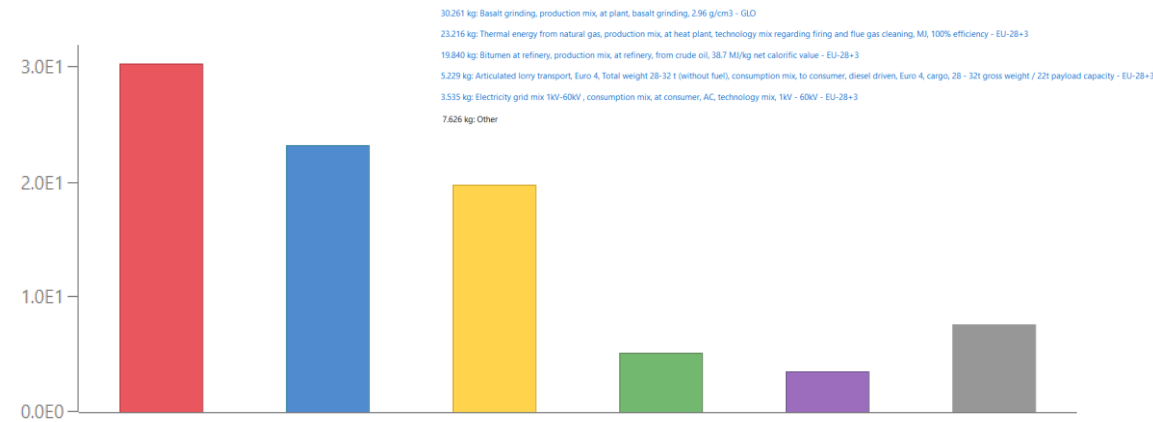

# Life Cycle Assessment of Two Asphalt Mixes – Asphalt Mix 2

## Inputs/Outputs - RAP Pretreatment

| Inputs                                     |                               |         |      |                |             |               |               |                 |          |
|--------------------------------------------|-------------------------------|---------|------|----------------|-------------|---------------|---------------|-----------------|----------|
| Flow                                       | Category                      | Amount  | Unit | Costs/Reven... | Uncertainty | Avoided wa... | Provider      | Data quality... | Location |
| Diesel consumption in construction machine | Materials production/Oth...   | 0.12000 | kg   |                | none        |               | Diesel c...   |                 |          |
| Electricity                                | Energy carriers and techno... | 3.00000 | MJ   |                | none        |               | Electricit... |                 |          |

## Inputs/Outputs - Raw Material Production\_SM

| Inputs            |                             |         |      |                |             |               |              |                 |          |
|-------------------|-----------------------------|---------|------|----------------|-------------|---------------|--------------|-----------------|----------|
| Flow              | Category                    | Amount  | Unit | Costs/Reven... | Uncertainty | Avoided wa... | Provider     | Data quality... | Location |
| Basalt (ground)   | Materials production/Oth... | 0.70000 | t    |                | none        |               | Basalt gr... |                 |          |
| Bitumen           | Materials production/Org... | 0.04000 | t    |                | none        |               | Bitumen...   |                 |          |
| Quartz sand (0/2) | Materials production/Oth... | 0.06000 | t    |                | none        |               | Quartz/S...  |                 |          |
| RAP               |                             | 0.20000 | t    |                | none        |               | RAP Pret...  |                 |          |

## Inputs/Outputs - Transport Mix materials\_SM

| Inputs    |                             |          |      |                |             |               |              |                 |          |
|-----------|-----------------------------|----------|------|----------------|-------------|---------------|--------------|-----------------|----------|
| Flow      | Category                    | Amount   | Unit | Costs/Reven... | Uncertainty | Avoided wa... | Provider     | Data quality... | Location |
| Transport | Materials production/Oth... | 6.00000  | tkm  |                | none        |               | Articulat... |                 |          |
| Transport | Materials production/Oth... | 8.00000  | tkm  |                | none        |               | Articulat... |                 |          |
| Transport | Materials production/Oth... | 70.00000 | tkm  |                | none        |               | Articulat... |                 |          |

## Inputs/Outputs - Asphalt plant operation


| Inputs                     |                               |           |      |                |             |               |               |                 |          |
|----------------------------|-------------------------------|-----------|------|----------------|-------------|---------------|---------------|-----------------|----------|
| Flow                       | Category                      | Amount    | Unit | Costs/Reven... | Uncertainty | Avoided wa... | Provider      | Data quality... | Location |
| Diesel consumption in c... | Materials production/Oth...   | 1.12000   | kg   |                | none        |               | Diesel c...   |                 |          |
| Electricity                | Energy carriers and techno... | 30.00000  | MJ   |                | none        |               | Electricit... |                 |          |
| Thermal energy (MJ)        | Energy carriers and techno... | 330.00000 | MJ   |                | none        |               | Thermal ...   |                 |          |

## Inputs/Outputs - Asphalt Mix


| Inputs                        |          |          |      |                |             |               |             |                 |          |
|-------------------------------|----------|----------|------|----------------|-------------|---------------|-------------|-----------------|----------|
| Flow                          | Category | Amount   | Unit | Costs/Reven... | Uncertainty | Avoided wa... | Provider    | Data quality... | Location |
| Material Manufactured         |          | 1.00000  | t    |                | none        |               | Asphalt ... |                 |          |
| Material transported to plant |          | 84.00000 | tkm  |                | none        |               | Transpor... |                 |          |
| Raw Material                  |          | 1.00000  | t    |                | none        |               | Raw Mat...  |                 |          |

| Outputs     |          |         |      |                |             |               |          |                 |          |
|-------------|----------|---------|------|----------------|-------------|---------------|----------|-----------------|----------|
| Flow        | Category | Amount  | Unit | Costs/Reven... | Uncertainty | Avoided pr... | Provider | Data quality... | Location |
| Asphalt mix |          | 1.00000 | t    |                | none        |               |          |                 |          |

Impact category Climate change

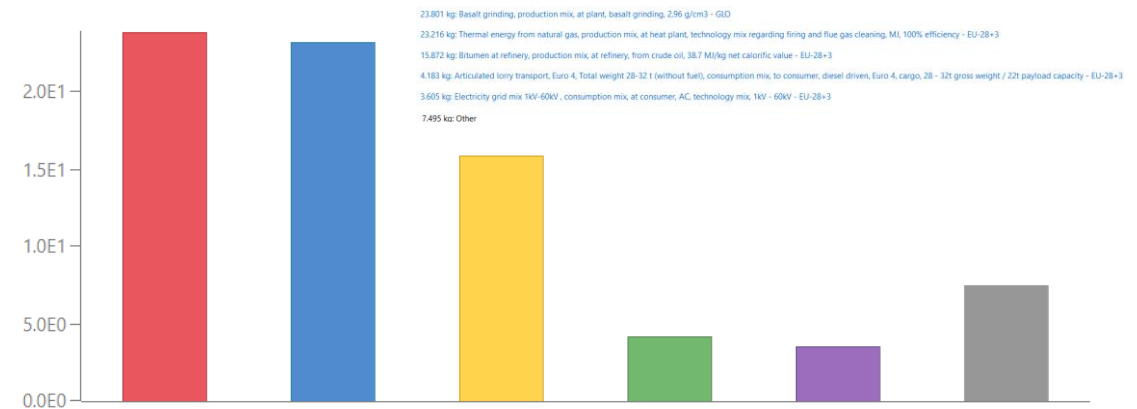

# Life Cycle Assessment of a Road Asphalt Pavement

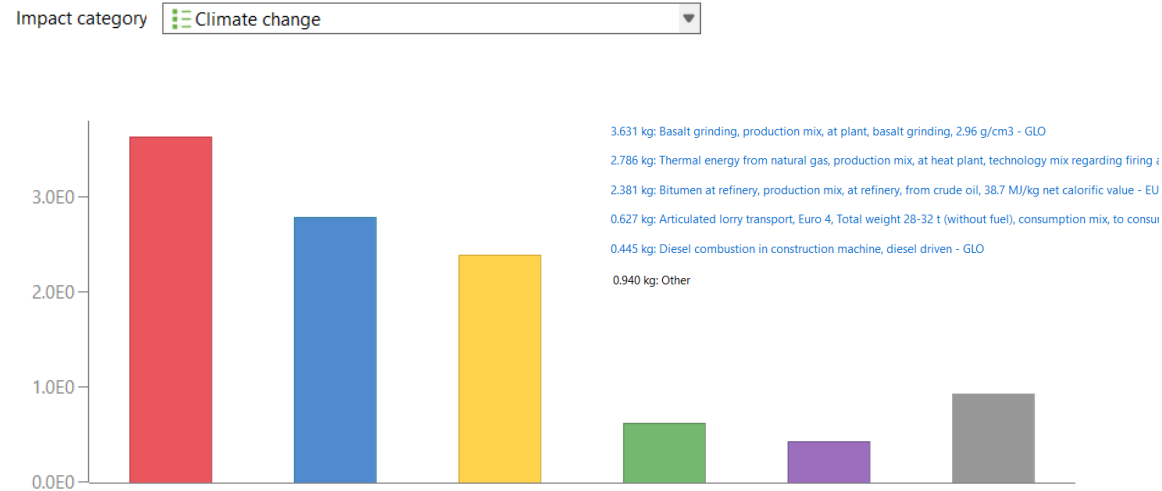

**Fossil resource use:** 377.5 MJ (105 kWh, almost 10 liters of diesel)

Main hotspot: Bitumen production (70%)

**Climate change impact:** 10.81 kg CO<sub>2</sub>-eq

Main hotspots: Basalt grinding, thermal energy from natural gas, and bitumen refining (80% combined)

- ❖ While the values for 0.12 tons may seem small, when scaled to full road construction projects, the energy demand and carbon footprint become highly significant.
- ❖ Impact analysis highlights bitumen, aggregate processing, and heating as the main areas for potential improvements

## Conventional Mixture

|                                                                                                        |                                  |             |
|--------------------------------------------------------------------------------------------------------|----------------------------------|-------------|
| Climate change                                                                                         | Environmental Footprint          | 10.81038 kg |
| Basalt grinding, production mix, at plant, basalt grinding, 2.96 g/cm <sup>3</sup> - GLO               | Materials production/Others      | 3.63138 kg  |
| Thermal energy from natural gas, production mix, at heat plant, technology mix regarding firing        | Energy carriers and technologies | 2.78587 kg  |
| Bitumen at refinery, production mix, at refinery, from crude oil, 38.7 MJ/kg net calorific value - EU  | Energy carriers and technologies | 2.38084 kg  |
| Articulated lorry transport, Euro 4, Total weight 28-32 t (without fuel), consumption mix, to consumer | Transport services/Road          | 0.62745 kg  |
| Diesel combustion in construction machine, diesel driven - GLO                                         | Materials production             | 0.44488 kg  |
| Electricity grid mix 1kV-230V                                                                          | Energy carriers and technologies | 0.42415 kg  |
| Quartz/Silica sand, single                                                                             | Materials production/Others      | 0.29387 kg  |
| Diesel mix at filling station                                                                          | Energy carriers and technologies | 0.22194 kg  |

|                                                                                                       |                                  |              |
|-------------------------------------------------------------------------------------------------------|----------------------------------|--------------|
| Resource use, fossils                                                                                 | Environmental Footprint          | 377.51423 MJ |
| Bitumen at refinery, production mix, at refinery, from crude oil, 38.7 MJ/kg net calorific value - EU | Energy carriers and technologies | 260.53698 MJ |
| Thermal energy from natural gas, production mix, at heat plant, technology mix regarding firing       | Energy carriers and technologies | 44.68002 MJ  |
| Basalt grinding, production mix, at plant, basalt grinding, 2.96 g/cm <sup>3</sup> - GLO              | Materials production/Others      | 42.88565 MJ  |
| Diesel mix at filling station                                                                         | Energy carriers and technologies | 17.50679 MJ  |
| Electricity grid mix 1kV-230V                                                                         | Energy carriers and technologies | 7.28897 MJ   |
| Quartz/Silica sand, single                                                                            | Materials production/Others      | 4.61581 MJ   |


## Mixture 20% RAP

|                                                                                                        |                                  |            |
|--------------------------------------------------------------------------------------------------------|----------------------------------|------------|
| Climate change                                                                                         | Environmental Footprint          | 9.64298 kg |
| Basalt grinding, production mix, at plant, basalt grinding, 2.96 g/cm <sup>3</sup> - GLO               | Materials production/Others      | 2.85614 kg |
| Thermal energy from natural gas, production mix, at heat plant, technology mix regarding firing        | Energy carriers and technologies | 2.78587 kg |
| Bitumen at refinery, production mix, at refinery, from crude oil, 38.7 MJ/kg net calorific value - EU  | Energy carriers and technologies | 1.90467 kg |
| Articulated lorry transport, Euro 4, Total weight 28-32 t (without fuel), consumption mix, to consumer | Transport services/Road          | 0.68123 kg |
| Diesel combustion in construction machine, diesel driven - GLO                                         | Materials production             | 0.45360 kg |
| Electricity grid mix 1kV-230V                                                                          | Energy carriers and technologies | 0.43263 kg |
| Quartz/Silica sand, single                                                                             | Materials production/Others      | 0.29387 kg |
| Diesel mix at filling station                                                                          | Energy carriers and technologies | 0.23496 kg |

|                                                                                                       |                                  |              |
|-------------------------------------------------------------------------------------------------------|----------------------------------|--------------|
| Resource use, fossils                                                                                 | Environmental Footprint          | 317.42417 MJ |
| Bitumen at refinery, production mix, at refinery, from crude oil, 38.7 MJ/kg net calorific value - EU | Energy carriers and technologies | 208.42959 MJ |
| Thermal energy from natural gas, production mix, at heat plant, technology mix regarding firing       | Energy carriers and technologies | 44.68002 MJ  |
| Basalt grinding, production mix, at plant, basalt grinding, 2.96 g/cm <sup>3</sup> - GLO              | Materials production/Others      | 33.73029 MJ  |
| Diesel mix at filling station                                                                         | Energy carriers and technologies | 18.53370 MJ  |
| Electricity grid mix 1kV-230V                                                                         | Energy carriers and technologies | 7.43475 MJ   |
| Quartz/Silica sand, single                                                                            | Materials production/Others      | 4.61581 MJ   |

Detailed Layout  
Single Family Residence, 310W 92nd ST

| ID | ID | Task Name                                                           | Duration | Start       | Finish       | CSI Codes                                   | 2023<br>H1 | H2 | 2024<br>H1 | H2 | 2025<br>H1 | H2 |
|----|----|---------------------------------------------------------------------|----------|-------------|--------------|---------------------------------------------|------------|----|------------|----|------------|----|
| 1  | 1  | Single Family Residence, 310 West 92nd ST.                          | 359 days | Mon 8/14/23 | Wed 1/8/25   |                                             |            |    |            |    |            |    |
| 2  | 2  | Key Dates and & Milestones                                          | 331 days | Thu 9/21/23 | Wed 1/8/25   |                                             |            |    |            |    |            |    |
| 3  | 3  | NTP                                                                 | 0 days   | Thu 9/21/23 | Thu 9/21/23  |                                             |            |    |            |    |            |    |
| 4  | 4  | Shop Drawing Start Date                                             | 0 days   | Wed 5/1/24  | Wed 5/1/24   |                                             |            |    |            |    |            |    |
| 5  | 5  | Submittals start date                                               | 0 days   | Sun 10/1/23 | Sun 10/1/23  |                                             |            |    |            |    |            |    |
| 6  | 6  | Submittals Finish date                                              | 0 days   | Mon 7/22/24 | Mon 7/22/24  |                                             |            |    |            |    |            |    |
| 7  | 7  | Final Completion                                                    | 0 days   | Wed 1/8/25  | Wed 1/8/25   |                                             |            |    |            |    |            |    |
| 8  | 8  | General Requiements                                                 | 5 days   | Mon 8/14/23 | Fri 8/18/23  |                                             |            |    |            |    |            |    |
| 9  | 9  | Clean up and remediate OSHA/DOB violations                          | 5 days   | Mon 8/14/23 | Fri 8/18/23  |                                             |            |    |            |    |            |    |
| 10 | 10 | Submittals                                                          | 305 days | Thu 9/21/23 | Sat 11/30/24 |                                             |            |    |            |    |            |    |
| 11 | 11 | Prepare & Submit                                                    | 219 days | Thu 9/21/23 | Sun 7/28/24  |                                             |            |    |            |    |            |    |
| 12 | 12 | P&S - Isolator location plan shop drawings                          | 282 days | Thu 9/21/23 | Fri 6/28/24  | 03050 Concrete – Music Studio Floor         |            |    |            |    |            |    |
| 13 | 13 | P&S - Pre-cast stone lintel and sill shop drawings                  | 131 days | Wed 2/21/24 | Sun 6/30/24  | 04000 MASONRY                               |            |    |            |    |            |    |
| 14 | 14 | P&S - New exterior metal railing shop drawings                      | 61 days  | Wed 5/1/24  | Sun 6/30/24  | 05586 Architectural Metals                  |            |    |            |    |            |    |
| 15 | 15 | P&S - New metal stair to Cellar shop drawings                       | 45 days  | Wed 5/1/24  | Fri 6/14/24  | 05586 Architectural Metals                  |            |    |            |    |            |    |
| 16 | 16 | P&S - Steel dunnage shop drawings                                   | 45 days  | Wed 5/1/24  | Fri 6/14/24  | 05586 Architectural Metals                  |            |    |            |    |            |    |
| 17 | 17 | P&S - AC Grille Submittal                                           | 45 days  | Wed 5/1/24  | Fri 6/14/24  | 05586 Architectural Metals                  |            |    |            |    |            |    |
| 18 | 18 | P&S - Custom medicine cabinets with nickel trim                     | 76 days  | Wed 5/1/24  | Mon 7/15/24  | 05586 Architectural Metals                  |            |    |            |    |            |    |
| 19 | 19 | P&S - Cabinet shop - shop drawings - Kitchen                        | 36 days  | Mon 6/10/24 | Mon 7/15/24  | 06406 Cabinet Shop                          |            |    |            |    |            |    |
| 20 | 20 | P&S - Cabinet shop - shop drawings - Library                        | 36 days  | Mon 6/10/24 | Mon 7/15/24  | 06406 Cabinet Shop                          |            |    |            |    |            |    |
| 21 | 21 | P&S - Cabinet shop - shop drawings - 4th floor master bedroom floor | 36 days  | Mon 6/10/24 | Mon 7/15/24  | 06406 Cabinet Shop                          |            |    |            |    |            |    |
| 22 | 22 | P&S - Cabinet shop - shop drawings - Kitchen cabinet door sample    | 21 days  | Mon 6/10/24 | Sun 6/30/24  | 06406 Cabinet Shop                          |            |    |            |    |            |    |
| 23 | 23 | P&S - Cabinet shop - shop drawings - Running Trim (misc.)           | 36 days  | Mon 6/10/24 | Mon 7/15/24  | 06406 Cabinet Shop                          |            |    |            |    |            |    |
| 24 | 24 | P&S - Main stair 1st fl. to Roof shop drawings                      | 31 days  | Sat 6/22/24 | Mon 7/22/24  | 06430 Wood Stairs & Handrails               |            |    |            |    |            |    |
| 25 | 25 | P&S - Main stair custom newel & volute – 1st fl. landing            | 31 days  | Sat 6/22/24 | Mon 7/22/24  | 06430 Wood Stairs & Handrails               |            |    |            |    |            |    |
| 26 | 26 | P&S - Music studio risers & handrail shop drawings                  | 31 days  | Sat 6/22/24 | Mon 7/22/24  | 06430 Wood Stairs & Handrails               |            |    |            |    |            |    |
| 27 | 27 | P&S - Metal door shop drawings                                      | 36 days  | Mon 6/10/24 | Mon 7/15/24  | 08100 Metal Doors                           |            |    |            |    |            |    |
| 28 | 28 | P&S - Elevator door shop drawings                                   | 36 days  | Mon 6/10/24 | Mon 7/15/24  | 08100 Metal Doors                           |            |    |            |    |            |    |
| 29 | 29 | P&S - Wood door shop drawings                                       | 45 days  | Sat 6/1/24  | Mon 7/15/24  | 08200 Wood Doors                            |            |    |            |    |            |    |
| 30 | 30 | P&S - Plaster shop drawings                                         | 31 days  | Fri 6/28/24 | Sun 7/28/24  | 09230 Plaster Mouldings                     |            |    |            |    |            |    |
| 31 | 31 | P&S - Stone & tile shop drawings                                    | 31 days  | Sat 6/22/24 | Mon 7/22/24  | 09300 Stone & Tile                          |            |    |            |    |            |    |
| 32 | 32 | P&S - Glass shower enclosure shop drawings                          | 31 days  | Sat 6/22/24 | Mon 7/22/24  | 09500 Glass & Mirror – shower enclosures    |            |    |            |    |            |    |
| 33 | 33 | P&S - Glass shop drawings (misc.)                                   | 31 days  | Sat 6/22/24 | Mon 7/22/24  | 09500 Glass & Mirror – kitchen backsplashes |            |    |            |    |            |    |
| 34 | 34 | P&S - Mechanical shop drawings                                      | 70 days  | Mon 4/22/24 | Sun 6/30/24  | 15700 HVAC - Ductwork                       |            |    |            |    |            |    |
| 35 | 35 | P&S - Radiator & motorized control valve submittals                 | 53 days  | Wed 5/1/24  | Sat 6/22/24  | 15700 HVAC – Hot Water Radiator             |            |    |            |    |            |    |
| 36 | 36 | P&S - Thermostat submittals                                         | 53 days  | Wed 5/1/24  | Sat 6/22/24  | 15700 HVAC – LG combo thermostats           |            |    |            |    |            |    |
| 37 | 37 | P&S - Radiant floor heat shop drawings                              | 21 days  | Mon 6/10/24 | Sun 6/30/24  | 15700 HVAC – Elec. radiant flr heat         |            |    |            |    |            |    |

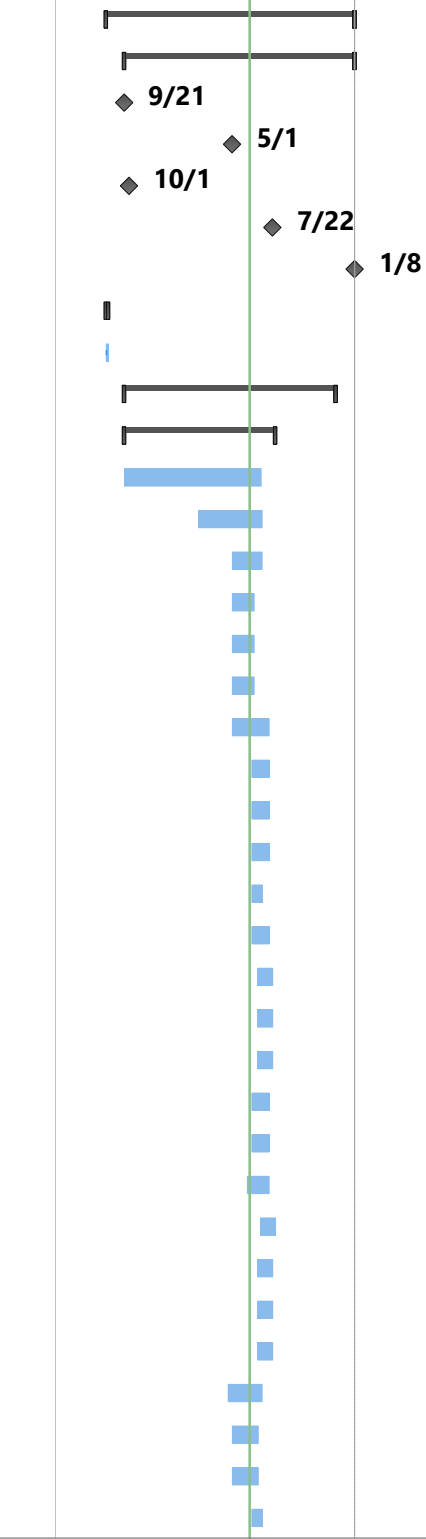

Date: Thu 6/6/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress


Manual Progress

↓

Detailed Layout  
Single Family Residence, 310W 92nd ST

| ID  | ID  | Task Name                                 | Duration | Start        | Finish       | CSI Codes                                | 2023<br>H1 | H2 | 2024<br>H1 | H2 | 2025<br>H1 | H2 |
|-----|-----|-------------------------------------------|----------|--------------|--------------|------------------------------------------|------------|----|------------|----|------------|----|
| 288 | 288 | Install mechanical trim-outs              | 57 days  | Mon 9/16/24  | Fri 12/6/24  | 15700 Mechanical                         |            |    |            |    |            |    |
| 289 | 289 | Install electrical trim-outs              | 57 days  | Mon 9/16/24  | Fri 12/6/24  | 16720 Electrical                         |            |    |            |    |            |    |
| 290 | 290 | Install Plumbing trim-outs                | 42 days  | Mon 10/7/24  | Fri 12/6/24  | 15400 Plumbing                           |            |    |            |    |            |    |
| 291 | 291 | Inspect MEP trim-outs                     | 1 day    | Mon 12/9/24  | Mon 12/9/24  | 01450 Testing and Inspection Services    |            |    |            |    |            |    |
| 292 | 292 | Existing stair caller finishing           | 41 days  | Tue 10/1/24  | Fri 11/29/24 | 09000 FINISHES                           |            |    |            |    |            |    |
| 293 | 293 | Final Paint                               | 23 days  | Fri 11/1/24  | Thu 12/5/24  | 09900 PAINTS AND COATINGS                |            |    |            |    |            |    |
| 294 | 294 | Install bathroom fittings and accessories | 3 days   | Thu 11/21/24 | Mon 11/25/24 | 15400 Plumbing                           |            |    |            |    |            |    |
| 295 | 295 | Install new metal railing                 | 3 days   | Thu 11/21/24 | Mon 11/25/24 | 09800 ACOUSTICAL TREATMENT               |            |    |            |    |            |    |
| 296 | 296 | Install Drapery                           | 11 days  | Mon 12/2/24  | Mon 12/16/24 | 12000 FURNISHINGS                        |            |    |            |    |            |    |
| 297 | 297 | Roof                                      | 79 days  | Thu 8/15/24  | Mon 12/9/24  |                                          |            |    |            |    |            |    |
| 298 | 298 | Interiors and finishing                   | 79 days  | Thu 8/15/24  | Mon 12/9/24  |                                          |            |    |            |    |            |    |
| 299 | 299 | Roof Demolition                           | 7 days   | Thu 8/15/24  | Fri 8/23/24  | 01900 Facility Demolition and Removal    |            |    |            |    |            |    |
| 300 | 300 | Roof Structural Work                      | 25 days  | Mon 8/26/24  | Mon 9/30/24  | 03500 CEMENTITIOUS DECKS AND UNDERLAYMEI |            |    |            |    |            |    |
| 301 | 301 | Roof Finishing Work                       | 10 days  | Tue 10/1/24  | Tue 10/15/24 | 09000 FINISHES                           |            |    |            |    |            |    |
| 302 | 302 | Rough Dunnage and FDNY clearance          | 4 days   | Wed 10/16/24 | Mon 10/21/24 | 07800 FIRE AND SMOKE PROTECTION          |            |    |            |    |            |    |
| 303 | 303 | Install mechanical trim-outs              | 39 days  | Thu 10/10/24 | Fri 12/6/24  | 15700 Mechanical                         |            |    |            |    |            |    |
| 304 | 304 | Install electrical trim-outs              | 39 days  | Thu 10/10/24 | Fri 12/6/24  | 16720 Electrical                         |            |    |            |    |            |    |
| 305 | 305 | Install Plumbing trim-outs                | 39 days  | Thu 10/10/24 | Fri 12/6/24  | 15400 Plumbing                           |            |    |            |    |            |    |
| 306 | 306 | Inspect MEP trim-outs                     | 40 days  | Thu 10/10/24 | Mon 12/9/24  | 01450 Testing and Inspection Services    |            |    |            |    |            |    |
| 307 | 307 | Install new exhaust fans                  | 40 days  | Thu 10/10/24 | Mon 12/9/24  | 15700 Mechanical                         |            |    |            |    |            |    |
| 308 | 308 | Install new gas generator                 | 3 days   | Fri 10/18/24 | Tue 10/22/24 | 15700 Mechanical                         |            |    |            |    |            |    |
| 309 | 309 | Install railing                           | 2 days   | Wed 10/23/24 | Thu 10/24/24 | 05520 Handrails and Railings             |            |    |            |    |            |    |
| 310 | 310 | Install louvers                           | 2 days   | Fri 10/25/24 | Mon 10/28/24 | 10720 Exterior Louvers                   |            |    |            |    |            |    |
| 311 | 311 | Close-Out                                 | 15 days  | Tue 12/17/24 | Wed 1/8/25   |                                          |            |    |            |    |            |    |
| 312 | 312 | Final Inspection                          | 5 days   | Tue 12/17/24 | Mon 12/23/24 | 01770 Closeout Procedures                |            |    |            |    |            |    |
| 313 | 313 | Owner's Punchlist                         | 5 days   | Tue 12/24/24 | Tue 12/31/24 | 01770 Closeout Procedures                |            |    |            |    |            |    |
| 314 | 314 | Punchlist Correction                      | 5 days   | Thu 1/2/25   | Wed 1/8/25   | 01770 Closeout Procedures                |            |    |            |    |            |    |

Date: Thu 6/6/24

|           |                                                                                     |                    |                                                                                       |                       |                                                                                       |                    |                                                                                       |                 |                                                                                       |
|-----------|-------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|-----------------|---------------------------------------------------------------------------------------|
| Task      |  | Project Summary    |  | Manual Task           |  | Start-only         |  | Deadline        |  |
| Split     |  | Inactive Task      |  | Duration-only         |  | Finish-only        |  | Progress        |  |
| Milestone |  | Inactive Milestone |  | Manual Summary Rollup |  | External Tasks     |  | Manual Progress |  |
| Summary   |  | Inactive Summary   |  | Manual Summary        |  | External Milestone |  |                 |                                                                                       |
